

CABLE & COMMUNICATIONS CORPORATION

904 C Avenue
P.O. Box 280
Circle, Montana 59215
Ph: (406) 485-3301

MASTER FILE

June 27, 2006

UPS SECOND DAY AIR

Kate Whitney
Administrator Utility Division
Montana Public Service Commission
1701 Prospect Avenue
Helena, MT 59620

RECEIVED BY
2006 JUN 29
10:44:28 AM
PUBLIC SERVICE
COMMISSION

RE: Cable & Communications Corporation's
Fourth Quarterly and Second Semi-Annual Report – PSC Order No. 6518a

Ms. Whitney:

Enclosed are an original and five copies of Cable & Communications Corporation's
Fourth Quarterly and Second Semi-Annual Report as required by the Final Order dated
April 7, 2005 (PSC Order No. 6518a).

Thank you.


Gerry Anderson
General Manager

Enclosure

RECEIVED BY
2006 JUN 29 PM 4: 28
PUBLIC SERVICE
COMMISSION

CABLE & COMMUNICATIONS CORPORATION'S
(d/b/a Mid-Rivers Cellular)

FOURTH QUARTERLY AND
SECOND SEMI-ANNUAL REPORT
AS REQUIRED BY FINAL ORDER DATED APRIL 7, 2005
(PSC Order No. 6518a)

Service Date: June 27, 2006

FOURTH QUARTERLY REPORT:

- I. Unsatisfied Requests –March 16 through June 15, 2006
 - a. By location in each of the two study areas:
 - Mid-Rivers Study Area = 0.
 - Range Study Area = 0.
 - b. Detailed description of why customer requests for service could not be satisfied.
 - There were no unsatisfied requests.

- II. Customer Complaints –March 16 through June 15, 2006.
 - a. Number and nature of complaints – see Attachments A and B.
 - b. Remedy employed to address complaints – see Attachments A and B.
 - c. Location of complaints by Study Area
 - Mid-Rivers – see Attachments A and B.
 - Range – see Attachment A.
 - d. Number of repeat complaints – see Attachments A and B.

NOTE: The complainant in Attachment B is not a current customer of Cable & Communications Corporation d/b/a Mid-Rivers Cellular.

- III. Federal Universal Service Funds, including Lifeline and Link Up Funds Received – March 16 through June 15, 2006
 - a. Funds received

- Interstate Common Line Support:
 1. \$32,845.00 received in April 2006 for February 2006.
 2. \$32,845.00 received in May 2006 for March 2006.
 3. \$32,632.00 received in June 2006 for April 2006.

- High Cost Loop Support:
 4. \$45,171.00 received in April 2006 for February 2006.
 5. \$45,171.00 received in May 2006 for March 2006.
 6. \$44,092.00 received in June 2006 for April 2006.

- Local Switching Support:
 7. \$9,593.00 received in April 2006 for February 2006.
 8. \$9,593.00 received in May 2006 for March 2006.
 9. \$9,572.00 received in June 2006 for April 2006.

- Lifeline and Link Up Funds:
 10. \$0 received to date.

SECOND SEMI-ANNUAL REPORT:

- IV. 5-Year Build-out Plan, updated for period of December 16, 2005, through June 15, 2006: see Attachment C.
- a. including expanded coverage in Northern Cheyenne Reservation, unless conflicting licenses, in which case an explanation of those conflicts must be provided:
- Representatives from Cable & Communications Corporation conducted an on-site meeting with Jace Killsback at the Northern Cheyenne Tribal Council in Lame Deer, Montana, on February 17, 2006.
 - See Attachment D and E hereto, which are letters addressed to Jace Killsback of the Northern Cheyenne Reservation dated May 15, 2006, and June 16, 2006, respectively, documenting repeated attempts to follow up regarding C&CC's desire to establish cellular services on the Northern Cheyenne Reservation.
- V. Reports on Progress in expanding wireless coverage. Reports are provided for those sites on which work has been commenced.
- a. Vida South Cell Site – see Attachment F
- b. North Lambert Cell Site – see Attachment G
- c. Alzada Cell Site – see Attachment H

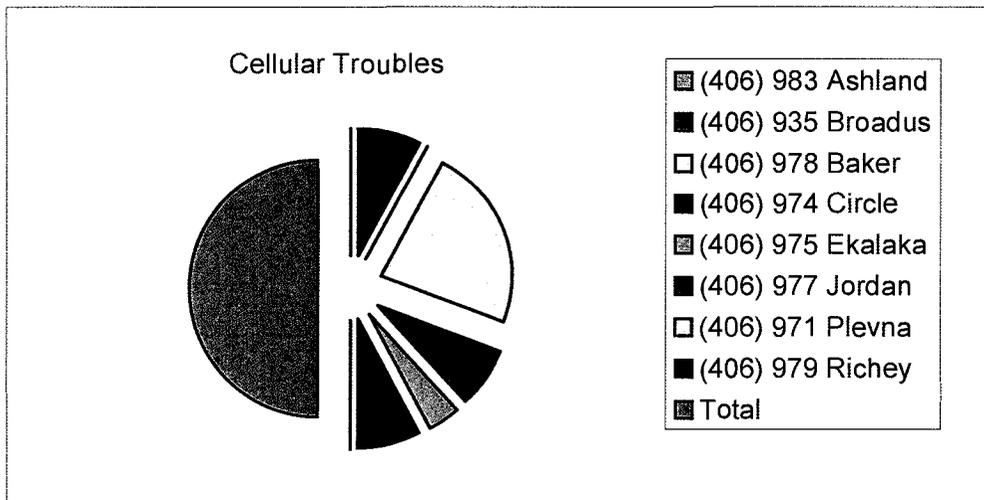
Attachment A

Mid-Rivers Cellular Quarterly Trouble Report

March 15, 2006 - June 15, 2006

- 17 - Total Cellular inquiries/troubles logged
- 4 - Alarms and troubles reported by other carrier's customer
- 13 - Troubles reported by Mid-Rivers Cellular Customers

Cellular Exchanges	Cellular Troubles	Out of Service	Repeat Troubles
<i>Range Study Area</i>			
(406) 983 Ashland	0	0	0
(406) 935 Broadus	2	0	0
<i>C&CC Study Area</i>			
(406) 978 Baker	6	0	1
(406) 974 Circle	2	0	0
(406) 975 Ekalaka	1	0	0
(406) 977 Jordan	2	0	0
(406) 971 Plevna	0	0	0
(406) 979 Richey	0	0	0
Total	13	0	1



Repeat Trouble: 2 different troubles reported for the same customer-- Nabor Well Services.
 First trouble was 1 cellular phone needed caller ID feature turned on
 Second trouble needed master reset to cell phone to get better reception in other areas.

Repair Time for Cellular Troubles	24 hours	48 hours	72 hours
Number of troubles repaired	11	2	0
Total in Percentages	85%	15%	0%

100% of troubles were dispatched and repaired within 48 hours.

2,346 - Total Mid-Rivers Cellular Customers
.55% Trouble Index for Mid-River's Cellular Customers (per 100 customers)

United States Government
Federal Communications Commission
Consumer and Governmental Affairs Bureau
Consumer Inquiries and Complaints Division
445 12th Street, SW, 4-C763
Washington, D.C. 20554

ATTACHMENT B

OFFICIAL

NOTICE OF INFORMAL COMPLAINT

Date: 6/16/06


THE COMPANY IDENTIFIED IN THE ATTACHED LIST IS REQUIRED TO RESPOND TO THIS NOTICE OF INFORMAL COMPLAINT WITHIN 30 DAYS OF THE DATE OF THIS NOTICE. Failure of any person to answer any lawful Commission inquiry is considered a misdemeanor punishable by a fine under Section 409(m) of the Communications Act (Act), 47 U.S.C. § 409(m). Further, failure to comply with any order of the Commission can result in prosecution under Section 401(b) of the Act, 47 U.S.C. § 401(b). Section 501 of the Act, 47 U.S.C. § 501, and Section 503(b)(1)(B) of the Act, 47 U.S.C. § 503(b)(1)(B), provide for forfeiture penalties against any person who willfully fails to follow the directives of the Act or of a Commission order. The Commission can impose forfeiture penalties of up to \$1.2 million for certain types of violations.

The attached list contains informal complaints that were filed with the Commission pursuant to Section 208 of the Act, 47 U.S.C. § 208, and Section 1.711 of the Commission's Rules, 47 C.F.R. § 1.711. A letter acknowledging your company's receipt of this Notice and of the enclosed complaint(s) should be sent to each consumer as soon as your company receives this Notice.

Pursuant to Sections 208 and 4(i) of the Act, 47 U.S.C. §§ 208, 154(i), we are forwarding a copy of the complaint(s) so that your company may satisfy or answer the complaint(s) based on a thorough review of all relevant records and other information. Your company should respond specifically to all material allegations raised in each complaint and summarize the actions taken by your company to satisfy the complaint.

Written responses must be filed with the Commission at 445 12th Street, SW, 4-C763, Washington, D.C. 20554. A separate response should be filed by each carrier for each case. Each response should include: (1) the complainant's name, and (2) the Case number. Companies are directed to send copies of their responses to consumers at the same time their responses are forwarded to the Commission. Each company required to respond to this Notice is directed to retain all records until final Commission disposition of the complaints.

If you have any questions regarding this Notice, please call the Consumer Inquiries and Complaints Division at (202) 418-2516, and leave a detailed message specifying the calling company name, the Case number, and the specific questions that you would like to have answered by the Bureau.


for Stephen E. Ebner, Acting Chief
Consumer Inquiries and Complaints Division

Attachment(s)

**List of Informal Complaints for Commission Action
06/16/06**

Carrier's Name**ICNumber****Complainant**

Mid-Rivers Telephone Coop., Inc.

06-R0064442

Micheal Johnson

Apparent Carrier: Mid-Rivers Telephone Coop., Inc.
 Complaint for: Micheal Johnson
 IC Number: 06-R0064442

Date Received: 6/7/2006 4:49:16 PM
 Service Date: 6/16/2006
 Response Date: 7/16/2006

COMPLAINT SUMMARY: mjohnson@truecos.com wrote on 6/1/2006 12:46:01 PM : ; I am writing in response to a situation that exists between two cell phone companies in my area. The two companies that I am referring to is Midrivers Communications and Alltel. These two companies, at the present time, are arguing over roaming charges on their towers.; I am located in Southeastern Montana. I have lived here for 3 years and have never had such poor communication services due to the above communication companies arguing over pennies. Alltel states, "that they will not pay for roaming time on Midrivers tours due to the exorbitant cost that Midrivers Communications is trying to charge." I do not know if this statement is true or not but this argument is creating areas around my community with no cell phone coverage. That leaves a lot of residents with no cell coverage, depending on which Cell phone company you have signed a service contract with. My other complaint is that neither company reveals this information until you have signed a two year agreement with that company.; I would like to find out how I can get the FCC involved to resolve this issue? These two companies are both showing large profits yearly. Due to their disagreement in cost, there are areas around Southeastern Montana that have no cell coverage. In our current world climate, this is unacceptable. This is an excellent example of two profitable companies putting pennies(profits) in front of our national security. Please let me know if there is more information that I can give to the FCC to resolve this issue.; Thanks.; Micheal C. Johnson; PO Box 1011; 325 Fallon County Rd; Baker, Mt 59313; Cell 406-891-0946; Hm 406-778-2449;

Problem Number:406-891-0946		
Title:	Contact Name:Micheal Johnson	
Last Name:Johnson	First Name:Micheal	Middle Initial:
Address: 325 Fallon County Road	City:Baker	State/Zip:MT, 59313
Contact Number:406-891-2449	Ext.:	Best Time to Call:
Fax Number:	Email Address:mjohnson@truecos.com	Internet Address:

Disputing charges listed on phone bill. **Total amount of dispute:**

Were any of the disputed charges paid?

Did the company billing for these charges adjust or refund some or all of the disputed charges?

If yes, the amount of the adjustment or refund:

Contacted the companies to resolve complaint?

If yes, was the complaint resolved to your satisfaction?

If yes, name of company, name and number of company representative you spoke with:

Name: Phone: Ext:

Date you spoke with company representative:

Willing to provide further written statements for use of the FCC or other agencies in enforcement actions against companies?

Mid-Rivers

TELEPHONE COOPERATIVE, INC.

P.O. Box 280 • 904 C Avenue
Circle, Montana 59215
(406) 485-3301 • Fax: (406) 485-2924
800-452-2288 • www.midrivers.com

June 16, 2006

**CERTIFIED MAIL/
RETURN RECEIPT REQUESTED**

Mr. Michael Johnson
325 Fallon County Road
Baker MT 59313

Mr. Johnson:

Mid-Rivers Telephone Cooperative, Inc. (the "Cooperative") received from the FCC a Notice of Informal Complaint (the "Notice") referencing your June 7, 2006 filing. The Cooperative is obligated under the FCC's Rules to acknowledge receipt of, and to respond to, the Notice.

The Cooperative and its wholly-owned subsidiary, Cable & Communications Corp. dba Mid-Rivers Cellular, plan to file a joint response to the Notice. We will provide you with a copy of our response to the FCC.


Gerry Anderson
General Manager

ATTACHMENT C

Updated 5-Year Build-Out Plan Cable & Communications Corporation d/b/a Mid-Rivers Cellular

- a. **2005 Plan** (in addition to the Digital Upgrade, which was completed on **November 11, 2005**):
 - i. Hammond cell site (45-12-13.4N / 104-55-33.1W)- **completed November 11, 2005**
 - ii. Baker II cell site (46-22-5.4N / 104-16-30.2W)- **completed November 11, 2005**
 - iii. Broadus II cell extender (45-26-55N / 105-24-38W)- **completed January 26, 2006**
 - iv. Ismay cell extender (46-24-05.0N / 104-48-09.0W)- **completed January 26, 2006**

- b. **2006 Plan:**
 - i. Vida South cell site (47-44-14.8N / 105-29-42.0W)- completing land acquisition
 - ii. North Lambert cell site (47-47-52.9N / 104-38-13.0W) - construction in progress
 - iii. Ashland West cell extender (45-37-38N / 106-30-23.2W)- exploring site location

- c. **2007 Plan:**
 - i. Alzada cell site (45-03-29.8N / 104-27-9.2W) –construction in progress

- d. **2008 Plan:**
 - i. Highway 59 cell site between Miles City and Broadus (45-57-17.5N / 105-39-9.9W) -exploring site location
 - ii. Weldon cell site (47-39-50.5N / 105-56-35W) -exploring site location

- e. **2009 Plan:**
 - i. Otter Creek cell site (45-21-39.8N / 105-50-27.8W) - exploring site location
 - ii. Cohagen cell site (47-02-49N / 106-40-52W) -exploring site location

ATTACHMENT D

Cable & Communications Corporation, dba

Mid-Rivers

C E L L U L A R

P.O. Box 280 • 904 C Avenue
Circle, Montana 59215
(406) 485-3301 • Fax: (406) 485-2924
www.midrivers.com

May 15, 2006

COPY

Jace Killsback
Northern Cheyenne Tribal Council
PO Box 128
Lame Deer, MT 59043

RE: Proposed Wireless Site

Jace:


Mid-Rivers Cellular met with you at Tribal Council headquarters in Lame Deer, Montana, on February 17, 2006. This meeting was attended by Mid-Rivers' employees: Gerry Anderson, Bill Wade, James Nash and Becky Schmidt.

At this meeting, Mid-Rivers explained its desire to serve the Northern Cheyenne area with wireless services, and requested consideration of its availability and expertise in constructing a site for this purpose. This letter is to follow up on our meeting with you and inquire about the completion of studies and any role we may be able to play in working with you on plans for wireless development on the Northern Cheyenne lands.

If we can be of any help in providing additional information or answering any questions, please feel free to contact Becky Schmidt at 406-687-7326 or James Nash at 406-687-7356.

Thank you for the opportunity to meet with you. We look forward to working with you.

Thank you.


Gerry Anderson
General Manager

ATTACHMENT E

Cable & Communications Corporation, dba

Mid-Rivers

C E L L U L A R

P.O. Box 280 • 904 C Avenue
Circle, Montana 59215
(406) 485-3301 • Fax: (406) 485-2924
www.midrivers.com

June 16, 2006

Jace Killsback
Northern Cheyenne Tribal Council
PO Box 128
Lame Deer, MT 59043

RE: Proposed Wireless Site

Jace:

Mid-Rivers Cellular wishes to again extend its offer to serve the Northern Cheyenne area with wireless services. If we can be of any help in providing additional information or answering any questions, please feel free to contact Becky Schmidt at 406-687-7326 or James Nash at 406-687-7356.

Thank you.


Gerry Anderson
General Manager

ATTACHMENT F

TIMELINE

Vida South

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Preliminary Analysis					
Initial Site Analysis	8/11/2005	11/1/2005	Completed	Clay	Survey filed
Preliminary Engineering	3/29/2006	5/11/2006		Jim Wilson	
Preliminary Environmental Review	5/11/2006	5/8/2006		Becky	Satisfactory Phase I Environmental Assessment
Preliminary Cultural Impact Review	5/11/2006	6/30/2006		Becky	
Preliminary Historical Impact Review	5/11/2006	6/30/2006		Becky	
Preliminary Geophysical Review	5/11/2006	6/30/2006		Becky	
Real Property - Site Procurement					
Ownership Report from Title Company	4/5/2006	6/8/2006		Becky	
Discussions with Landowner	9/27/2005	6/23/2006		Becky	
Documentation of site use arrangements	6/12/2006	6/30/2006		Becky	Warranty Deed
Federal Aviation Administration (FAA)					
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	3/30/2006	4/7/2006		Becky	
Federal Communications Commission (FCC)					
Antenna Structure Registration					Not Applicable
Attorney to file cellular Phase II Application w/FCC	5/11/2006	5/23/2006		Sylvia Lesse	
FCC Public Notice -- cellular	5/31/2006	5/31/2006		Sylvia Lesse	
FCC approval notice -- cellular	7/31/2006	8/31/2006		Sylvia Lesse	
Cellular license issued by FCC	8/31/2006	9/30/2006		Sylvia Lesse	
Site interconnection arrangements					Not Applicable - Mid-Rivers Tel.
If microwave coordination:			N/A		
Attorney to file microwave application w/FCC			N/A		
FCC Public Notice -- microwave			N/A		
FCC approval notice -- microwave			N/A		
Microwave license issued by FCC			N/A		

ATTACHMENT F

TIMELINE

Vida South

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Engineering - MRC (in house)					
Prepare cellular radio installation specifications & contract	1/2/2006	1/5/2006	Completed	James	Nortel & Crystal Telecom - Quotes received
Submit cellular radio installation specifications & contract to contractors for quotes	1/5/2006	6/12/2006	In Progress	James	Sent to Nortel 6/12/06
Finalize cellular contract		6/30/2006		James	
Contractor to install cellular radio	8/23/2006	9/22/2006		James	
Prepare microwave radio installation specifications & contract			N/A		
Submit microwave radio installation specifications & contract to contractors for quotes			N/A		
Finalize microwave contract			N/A		
Contractor to install microwave radio			N/A		
Prepare misc. equipment, hardware and power plant specifications	4/15/2006	6/13/2006	Completed	Clay	Quotes received from PPS & Action Battery - reviewing battery options
Purchase misc. equipment, hardware and power plant	6/13/2006	6/23/2006	In Progress	Clay	
Delivery of misc. equipment, hardware and power plant	6/26/2006	8/15/2006		Clay	
MRC personnel to install misc. equipment, hardware and power plant	8/16/2006	8/30/2006		Dustin/Clay	
Interconnection Agreement					
Building					
Building permit (local and/or state)	6/16/2006	6/30/2006		Clay	
Foundation & gen. slab installation by MRC personnel	7/30/2006	8/15/2006		Dustin/Clay	
Prepare building specifications & contract			N/A		In Stock
Submit building specifications & contract to contractors for quotes			N/A		In Stock
Finalize contract to purchase building			N/A		In Stock
Building delivery to MRC Supply			N/A		In Stock
Quotes for Offloading Building	7/3/2006	7/15/2006		Clay	at location
Offload Building		8/15/2006		Dustin/Clay	at location
Rekey Building		6/30/2006		Dustin/Clay	

ATTACHMENT F

TIMELINE

Vida South

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Quotes for MRTC Sign	6/21/2006	6/28/2006		Clay	
MRTC Sign Installation	8/15/2006	8/30/2006		Dustin/Clay	
Site development & landscaping by MRC personnel	8/15/2006	8/30/2006		Dustin/Clay	
Provide building information to COE/Network Engineer for inclusion in company database		8/30/2006		Clay	
Tower					
Obtain structural analysis of existing tower, if any			N/A		
Obtain Geotechnical Soil Survey	4/25/2006	6/30/2006	In Progress	Clay	Bids received sent contract 6/8/06
Prepare tower and antenna specifications & contract	6/1/2006	6/16/2006	In Progress	Clay	
Submit tower and antenna specifications & contract to contractors w/request for quotes	6/16/2006	6/30/2006	In Progress	Clay	
Finalize contract	7/3/2006	7/14/2006		Clay	
Contractor to complete contract & install tower and antenna(s)	7/17/2006	8/15/2006		Clay	
Contractor to post antenna structure registration number on tower		8/15/2006		Mike S./Clay	
Generator					
Purchase Generator, ATS	4/24/2006	6/30/2006		Clay	Sent RFP on 4/24/06 - No response will follow up
Delivery of Generator, ATS	7/3/2006	7/31/2006		Clay	
Test & Turn-up Generator	8/15/2006	8/30/2006		Dustin/Clay	
Provide generator information to COE/Network Engineer for inclusion in company database		8/30/2006		Clay	
Power					
Provide local power utility company information on electrical line required		3/6/2006	Completed	Clay	
Power utility company Install electrical lines	7/30/2006	8/15/2006		Clay	
Provide local power utility company information on gas line requirements				Clay/Dustin	Generator
Power utility company install gas lines				Clay/Dustin	Generator
Misc. Electrical Contract					
Quotes for Misc. Electrical	6/5/2006	6/23/2006		Clay	
Award Contract		6/30/2006		Clay	
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work		7/15/2006		Clay	

ATTACHMENT F

TIMELINE

Vida South

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Contractor to Provide Warranty Info on Installed Equipment					
Work Order					
Purchase Equipment for Work Order		7/3/2006		Clay	
Delivery of Equipment	7/4/2006	8/15/2006		Barb S./Clay	
Install Equipment	8/15/2006	8/30/2006		Mike S./Clay	
Issue Work Order		6/30/2006		Clay	
Misc. Items					
Equipment testing and turn up	8/30/2006	9/15/2006		Mike S.	
Advise COE/Network Engineer of date of turn up for entry in company database		9/30/2006		Mike S.	

ATTACHMENT G

TIMELINE

North Lambert

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Preliminary Analysis					
Initial Site Analysis	10/7/2005	5/18/2006	COMPLETE	Clay	
Preliminary Engineering	5/18/2006	6/12/2006	COMPLETE	Jim Wilson	
Preliminary Environmental Review	5/18/2006	6/30/2006		Becky	
Preliminary Cultural Impact Review	5/18/2006	6/30/2006		Becky	
Preliminary Historical Impact Review	5/18/2006	6/30/2006		Becky	
Preliminary Geophysical Review	5/18/2006	6/30/2006		Becky	
Real Property - Site Procurement					
Ownership Report from Title Company	6/28/2006	7/6/2006		Becky	
Discussions with Landowner	10/7/2005	5/7/2006		Becky	
Documentation of site use arrangements	5/8/2006	5/8/2006		Becky	
Federal Aviation Administration (FAA)					
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	6/6/2006	7/14/2006		Becky	
Federal Communications Commission (FCC)					
Antenna Structure Registration					Not Applicable
Attorney to file cellular Phase II Application w/FCC	6/12/2006	6/28/2006		Sylvia Lesse	
FCC Public Notice -- cellular	7/12/2006	7/19/2006		Sylvia Lesse	
FCC approval notice -- cellular	9/12/2006	9/30/2006		Sylvia Lesse	
Cellular license issued by FCC	10/15/2006	10/30/2006		Sylvia Lesse	
Site interconnection arrangements					Not Applicable - Mid-Rivers Tel.
If microwave coordination:			N/A		
Attorney to file microwave application w/FCC			N/A		
FCC Public Notice -- microwave			N/A		
FCC approval notice -- microwave			N/A		
Microwave license issued by FCC			N/A		

ATTACHMENT G

TIMELINE

North Lambert

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Engineering - MRC (in house)					
Prepare cellular radio installation specifications & contract	1/2/2006	1/5/2006	Completed	James	Nortel & Crystal Telecom - Quotes received
Submit cellular radio installation specifications & contract to contractors for quotes	1/5/2006	6/12/2006	In Progress	James	Sent to Nortel 6/12/06
Finalize cellular contract		6/30/2006		James	
Contractor to install cellular radio	9/5/2006	9/22/2006			
Prepare microwave radio installation specifications & contract			N/A		
Submit microwave radio installation specifications & contract to contractors for quotes			N/A		
Finalize microwave contract			N/A		
Contractor to install microwave radio			N/A		
Prepare misc. equipment, hardware and power plant specifications	4/15/2006	6/13/2006	Completed	Clay	
Purchase misc. equipment, hardware and power plant	6/13/2006	6/23/2006	In Progress	Clay	
Delivery of misc. equipment, hardware and power plant	6/26/2006	8/15/2006		Clay	
MRC personnel to install misc. equipment, hardware and power plant	8/30/2006	9/15/2006		Dustin/Clay	
Interconnection Agreement					
Building					
Building permit (local and/or state)	6/16/2006	6/30/2006		Clay	
Foundation & gen. slab installation by MRC personnel	8/15/2006	8/31/2006		Dustin/Clay	
Prepare building specifications & contract			N/A		
Submit building specifications & contract to contractors for quotes			N/A		
Finalize contract to purchase building			N/A		
Building delivery to MRC Supply			N/A		
Quotes for Offloading Building	7/3/2006	7/15/2006		Clay	
Offload Building		8/30/2006		Dustin/Clay	
Rekey Building		6/30/2006		Dustin/Clay	

ATTACHMENT G

TIMELINE

North Lambert

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Quotes for MRTC Sign	6/21/2006	6/28/2006		Clay	
MRTC Sign Installation		9/15/2006		Dustin/Clay	
Site development & landscaping by MRC personnel	8/30/2006	9/15/2006		Dustin/Clay	
Provide building information to COE/Network Engineer for inclusion in company database		9/15/2006		Clay	
Tower					
Obtain structural analysis of existing tower, if any			N/A		
Obtain Geotechnical Soil Survey	4/25/2006	6/30/2006	In Progress	Clay	Bids received sent contract 6/8/06
Prepare tower and antenna specifications & contract	6/1/2006	6/16/2006	In Progress	Clay	
Submit tower and antenna specifications & contract to contractors w/request for quotes	6/16/2006	6/30/2006	In Progress	Clay	
Finalize contract	7/3/2006	7/14/2006		Clay	
Contractor to complete contract & install tower and antenna(s)	7/17/2006	8/30/2006		Clay	
Contractor to post antenna structure registration number on tower		8/30/2006		Mike S./Clay	
Generator					
Purchase Generator, ATS	4/24/2006	6/30/2006		Clay	Sent RFP on 4/24/06 - No response will follow up
Delivery of Generator, ATS	7/3/2006	7/31/2006		Clay	
Test & Turn-up Generator	8/30/2006	9/15/2006		Dustin/Clay	
Provide generator information to COE/Network Engineer for inclusion in company database		8/30/2006		Clay	
Power					
Provide local power utility company information on electrical line required		5/24/2006	Completed	Clay	
Power utility company Install electrical lines	8/15/2006	8/30/2006		Clay	
Provide local power utility company information on gas line requirements				Clay/Dustin	Generator
Power utility company install gas lines				Clay/Dustin	Generator
Misc. Electrical Contract					
Quotes for Misc. Electrical	6/5/2006	6/23/2006	In Progress	Clay	
Award Contract		6/30/2006		Clay	
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work		7/15/2006			

ATTACHMENT G

TIMELINE

North Lambert

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Contractor to Provide Warranty Info on Installed Equipment					
Work Order					
Purchase Equipment for Work Order		7/17/2006		Clay	
Delivery of Equipment	7/18/2006	8/30/2006		Clay	
Install Equipment	8/30/2006	9/15/2006		Clay	
Issue Work Order		7/15/2006		Clay	
Misc. Items					
Equipment testing and turn up	9/15/2006	10/15/2006		Mike S.	
Advise COE/Network Engineer of date of turn up for entry in company database		10/30/2006		Mike S.	

ATTACHMENT H

TIMELINE

Alzada

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Preliminary Analysis					
Initial Site Analysis	6/12/2004	4/25/2006	COMPLETE	Clay	
Preliminary Engineering	4/26/2006	5/31/2006	COMPLETE	Jim Wilson	
Preliminary Environmental Review	5/18/2006	6/30/2006		Becky	
Preliminary Cultural Impact Review	5/18/2006	6/30/2006		Becky	
Preliminary Historical Impact Review	5/18/2006	6/30/2006		Becky	
Preliminary Geophysical Review	5/18/2006	6/30/2006		Becky	
Real Property - Site Procurement					
Ownership Report from Title Company	4/5/2006	4/6/2006	COMPLETE	Becky	
Discussions with Landowner	6/12/2004	5/4/2006	COMPLETE	Becky	
Documentation of site use arrangements	6/12/2004	5/4/2006	COMPLETE	Becky	Lease
Federal Aviation Administration (FAA)					
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	5/25/2006	6/30/2006		Becky	Aeronautical Study No. 2006-ANM-1162-OE assigned.
Federal Communications Commission (FCC)					
Antenna Structure Registration					Not Applicable
Attorney to file cellular Phase II Application w/FCC	5/31/2006	6/30/2006		Sylvia Lesse	
FCC Public Notice -- cellular	7/12/2006	7/19/2006		Sylvia Lesse	
FCC approval notice -- cellular	9/12/2006	9/30/2006		Sylvia Lesse	
Cellular license issued by FCC	10/15/2006	10/30/2006		Sylvia Lesse	
Site interconnection arrangements	6/6/2006	8/6/2006		Becky	Attorney drafting letter to Range Tel.
If microwave coordination:					
Attorney to file microwave application w/FCC					Waiting for approval
FCC Public Notice -- microwave					Waiting for approval
FCC approval notice -- microwave					Waiting for approval
Microwave license issued by FCC					Waiting for approval

ATTACHMENT H

TIMELINE

Alzada

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Engineering - MRC (in house)					
Prepare cellular radio installation specifications & contract	1/2/2006	1/5/2006	Completed	James	Nortel & Crystal Telecom - Quotes received
Submit cellular radio installation specifications & contract to contractors for quotes	1/5/2006	6/12/2006	In Progress	James	Sent to Nortel 6/12/06
Finalize cellular contract		6/30/2006		James	
Contractor to install cellular radio	9/15/2006	9/22/2006			
Prepare microwave radio installation specifications & contract	3/17/2006	6/30/2006	In Progress	Clay	Waiting on MW approval for site
Submit microwave radio installation specifications & contract to contractors for quotes	7/3/2006	7/17/2006		Clay	
Finalize microwave contract	7/17/2006	7/21/2006		Clay	
Contractor to install microwave radio	9/15/2006	9/30/2006		Clay	
Prepare misc. equipment, hardware and power plant specifications	4/15/2006	6/13/2006	Completed	Clay	
Purchase misc. equipment, hardware and power plant	6/13/2006	6/23/2006	In Progress	Clay	
Delivery of misc. equipment, hardware and power plant	6/26/2006	8/30/2006		Dustin/Clay	Power Bay installation by Contractor ?
MRC personnel to install misc. equipment, hardware and power plant	9/15/2006	9/30/2006		Dustin/Clay	
Interconnection Agreement					
Building					
Building permit (local and/or state)	6/16/2006	6/30/2006		Clay	
Foundation & gen. slab installation by MRC personnel	8/31/2006	9/15/2006			
Prepare building specifications & contract			N/A		In Stock
Submit building specifications & contract to contractors for quotes			N/A		In Stock
Finalize contract to purchase building			N/A		In Stock
Building delivery to MRC Supply			N/A		In Stock
Quotes for Offloading Building	7/3/2006	7/15/2006		Clay	
Offload Building		9/15/2006		Dustin/Clay	
Rekey Building		6/30/2006		Dustin/Clay	

ATTACHMENT H

TIMELINE

Alzada

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Quotes for MRTC Sign	6/21/2006	6/28/2006		Clay	
MRTC Sign Installation		9/29/2006		Dustin/Clay	
Site development & landscaping by MRC personnel	9/15/2006	9/29/2006		Dustin/Clay	
Provide building information to COE/Network Engineer for inclusion in company database		9/29/2006		Clay	
Tower					
Obtain structural analysis of existing tower, if any			N/A		Hammond Tower predisigned for additional MW dishes.
Obtain Geotechnical Soil Survey	4/25/2006	6/30/2006	In Progress	Clay	Bids received sent contract 6/8/06
Prepare tower and antenna specifications & contract	6/1/2006	6/16/2006	In Progress	Clay	
Submit tower and antenna specifications & contract to contractors w/request for quotes	6/16/2006	6/30/2006	In Progress	Clay	
Finalize contract	7/3/2006	7/14/2006		Clay	
Contractor to complete contract & install tower and antenna(s)	7/17/2006	9/15/2006		Clay	
Contractor to post antenna structure registration number on tower		9/15/2006		Mike S./Clay	
Generator					
Purchase Generator, ATS	4/24/2006	6/30/2006		Clay	Sent RFP on 4/24/06 - No response will follow up
Delivery of Generator, ATS	7/3/2006	7/31/2006		Clay	
Test & Turn-up Generator	9/15/2006	9/29/2006		Dustin/Clay	
Provide generator information to COE/Network Engineer for inclusion in company database		8/30/2006		Clay	
Power					
Provide local power utility company information on electrical line required		5/22/2006	Completed	Clay	
Power utility company Install electrical lines	8/30/2006	9/15/2006		Clay	
Provide local power utility company information on gas line requirements				Clay/Dustin	Generator
Power utility company install gas lines				Clay/Dustin	Generator
Misc. Electrical Contract					
Quotes for Misc. Electrical	6/5/2006	6/23/2006	In Progress	Clay	
Award Contract	6/30/2006			Clay	
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work		7/15/2006			

ATTACHMENT H

TIMELINE

Alzada

ACTION ITEM	START DATE	ESTIMATED COMPLETE DATE	STATUS	RESPONSIBLE PERSON / ENTITY	COMMENTS
Contractor to Provide Warranty Info on Installed Equipment					
Work Order					
Purchase Equipment for Work Order		7/31/2006			
Delivery of Equipment	8/1/2006	9/15/2006			
Install Equipment	9/15/2006	9/30/2006			
Issue Work Order		7/30/2006			
Misc. Items					
Equipment testing and turn up	9/30/2006	1Q 2007			
Advise COE/Network Engineer of date of turn up for entry in company database		11/15/2006			
