


Box 106



CABLE & COMMUNICATIONS CORPORATION

904 C Avenue
P.O. Box 280
Circle, Montana 59215
Ph: (406) 485-3301

MASTER FILE
Computer Indexed

June 29, 2007

VIA UPS NEXT DAY AIR

Kate Whitney
Montana Public Service Commission
1701 Prospect Avenue
Helena, MT 59620-2601

RE: Cable & Communications Corporation dba Mid-Rivers Cellular
Eighth Quarterly and Fourth Semi-Annual Report as Required
By Final Order 6518a
Docket No. D2003.8.105

RECEIVED BY
2007 JUL - 2 A 9: 28
PUBLIC SERVICE
COMMISSION

Ms. Whitney:

Enclosed for filing are an original and ten (10) copies of Cable & Communications Corporation dba Mid-Rivers Cellular's Eighth Quarterly and Fourth Semi-Annual Report as Required by Final Order 6518a in the above-referenced docket. Also enclosed is a disk with an electronic (pdf/Adobe Acrobat) copy of the document.

Feel free to contact me if you have any questions.

Thank you.

Gerry Anderson
General Manager

Enclosures

DISK RCVD

RECEIVED BY

2007 JUL -2 A 9:28

PUBLIC SERVICE
COMMISSION

DEPARTMENT OF PUBLIC SERVICE REGULATION
BEFORE THE PUBLIC SERVICE COMMISSION
OF THE STATE OF MONTANA

IN THE MATTER OF THE PETITION OF)	UTILITY DIVISION
CABLE & COMMUNICATIONS)	
CORPORATION, dba MID-RIVERS)	DOCKET NO. D2003.8.105
CELLULAR, for Designation as an Eligible)	
Telecommunications Carrier)	

CABLE & COMMUNICATIONS CORPORATION,
dba MID-RIVERS CELLULAR'S
EIGHTH QUARTERLY AND FOURTH SEMI-ANNUAL REPORT
AS REQUIRED BY FINAL ORDER DATED MARCH 29, 2005
(PSC Order No. 6518a)

Service Date: June 29, 2007

EIGHTH QUARTERLY REPORT

- I. Unsatisfied Requests – March 16 through June 15, 2007:
 - a. By location in each of the two study areas:
 - i. Mid-Rivers Study Area: zero (0).
 - ii. Range Study Area: zero (0).
 - b. Detailed description of why customer requests for service could not be satisfied: there were no unsatisfied requests.

- II. Customer Complaints – March 16 through June 15, 2007:
 - a. Number and nature of complaints: see Attachment A hereto.
 - b. Remedy employed to address complaints: see Attachment A hereto.
 - c. Location of complaints by Study Area:
 - i. Mid-Rivers: see Attachment A hereto.
 - ii. Range: see Attachment A hereto.
 - d. Number of repeat complaints: see Attachment A hereto.

- III. Federal Universal Service Funds, including Lifeline and Link Up Funds received – March 16 through June 15, 2007:
 - a. Funds received:
 - i. Interstate Common Line Support:
 1. \$31,238.00 received in April 2007 for February 2007.
 2. \$31,328.00 received in May 2007 for March 2007.
 3. \$31,777.00 received in June 2007 for April 2007.

ii. High Cost Loop Support:

1. \$45,356.00 received in April 2007 for February 2007.
2. \$45,356.00 received in May 2007 for March 2007.
3. \$46,321.00 received in June 2007 for April 2007.

iii. Local Switching Support:

1. \$9,154.00 received in April 2007 for February 2007.
2. \$9,154.00 received in May 2007 for March 2007.
3. \$9,295.00 received in June 2007 for April 2007.

iv. Lifeline and Link Up Funds:

1. \$0 received to date.

NOTE:

- (a) Included as Attachment B hereto is an excerpt including a section entitled "Lifeline, Link-Up & Toll Blocking" from the March/April 2007 issue of the *411* magazine published by Mid-Rivers Communications for its customers.

FOURTH SEMI-ANNUAL REPORT

IV. 5-Year Build-out Plan, updated for the period of December 16, 2006, through June 15, 2007: see Attachment C hereto.

a. Including expanded coverage in Northern Cheyenne Reservation, unless conflicting licenses, in which case an explanation of those conflicts must be provided:

i. Representatives from Cable & Communications Corporation conducted an on-site meeting with Jace Killsback at the Northern Cheyenne Tribal Council in Lame Deer, Montana, on February 17, 2006.

ii. Letters addressed to Jace Killsback of the Northern Cheyenne Reservation dated May 15, 2006, and June 16, 2006, were filed with the Commission in Cable & Communications Corporation's Second Semi-Annual Report of June 27, 2006. No response has been received to date.

iii. A letter addressed to Jace Killsback of the Northern Cheyenne Reservation dated March 20, 2007, was mailed via certified mail/return receipt requested and was signed in receipt on March 21, 2007. This letter and return receipt are attached hereto as Attachment D.

V. Reports on Progress in expanding wireless coverage. Reports are provided for those sites on which work has been commenced.

- a. Alzada Cell Site: see Attachment E hereto.
- b. Volborg Cell Site: see Attachment F hereto.
- c. Sheep Mountain Cell Site: see Attachment G hereto.
- d. Ismay CDMA Upgrade: see Attachment H hereto.
- e. Savage Cell Site: see Attachment I hereto.

RATE PLAN

- VI. The Final Order requires that Mid-Rivers Cellular must have on file with the Montana Public Service Commission (MTPSC) a copy of each rate plan that it offers for which it may receive FUSF support, including rates, terms and conditions of service: see Attachment J hereto.


Attachment A

Mid-Rivers Cellular Quarterly Trouble Report

March 15, 2007 - June 15, 2007

- 14 - Total Cellular inquiries/troubles logged
- 7 - Alarms and troubles reported by other carrier's customers
- 7 - Troubles reported by Mid-Rivers Cellular Customers

Cellular Exchanges	Cellular Troubles	Out of Service	Repeat Troubles
Range Study Area			
(406) 983 Ashland	0	0	0
(406) 935 Broadus	2	0	0
C&CC Study Area			
(406) 978 Baker	4	0	0
(406) 974 Circle	0	0	0
(406) 975 Ekalaka	0	0	0
(406) 977 Jordan	1	0	0
(406) 971 Plevna	0	0	0
(406) 979 Richey	0	0	0
(406) 928 Grass Range	0	0	0
(406) 954 Roy	0	0	0
Total	7	0	0

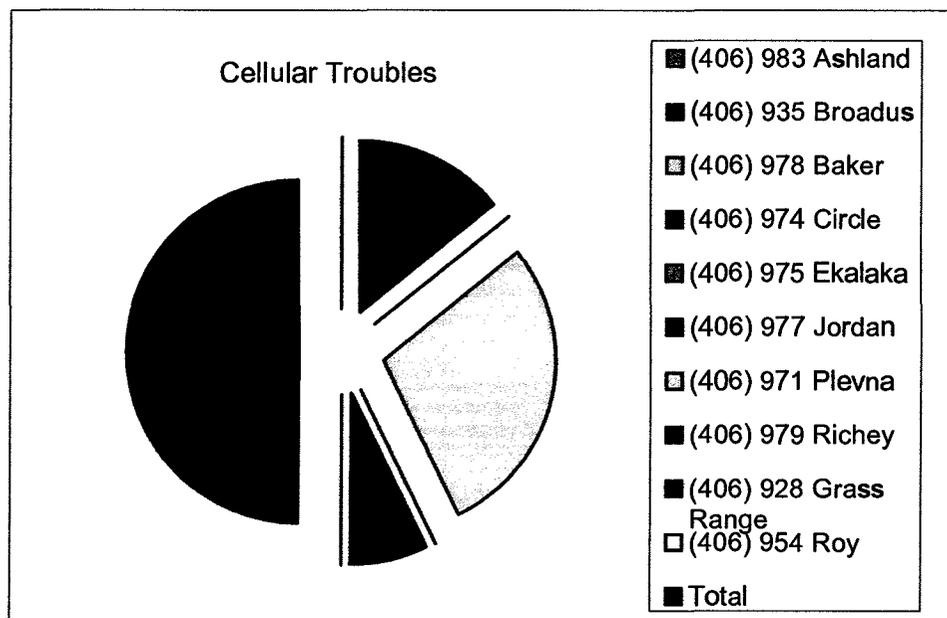

Repair Time for Cellular Troubles	24 hours	48 hours	72 hours
Number of troubles repaired	7	N/A	N/A
Total in Percentages	100%	N/A	N/A

100% of troubles were dispatched and repaired within 24 hours.

2,572 - Total Mid-Rivers Cellular Customers
.27% Trouble Index for Mid-River's Cellular Customers (per 100 customers)

Mid-Rivers Internet subscribers were e-mailed an Internet newsletter in April. This free monthly feature includes alerts on virus threats, e-mail scams, recommended websites, tips on using the Internet, tutorials on computer issues and information from Mid-Rivers Internet.

The Mid-Rivers Internet newsletter is only sent to Mid-Rivers customers' e-mail addresses and not to e-mail addresses such as yahoo or hotmail. Customers are given the option to halt the e-mailing of the newsletter to their e-mail address, if they so desire.

Mid-Rivers Internet looks forward to this newsletter service as helping to enhance its customers Internet experience.

Various state agencies, including the Office of Higher Education and Departments of Labor, Agriculture, Commerce, and others have been provided the authority to award the WIRED funds to bio-industry development projects within a 32-county region of Eastern and Central Montana. The goal of the Montana WIRED program is to develop a sustainable industry in these rural areas, create high-p

In late January 2007, five W assistance. More recently, bo... and Miles Community College (MCC) in Miles City were awarded WIRED funds for the development of job training programs and curriculum in the field.

DCC will partner with the MSU-Billings College of Technology to develop local expertise in the biomass/biofuels processing arena. MCC's project identifies a need for producers to have training in the bioproducts and biofuels industry, and will involve developing a WIRED Educational Consortium committed to providing the education and training necessary to promote biofuels and bioproducts economic development in Eastern and Central Montana.

The educational WIRED grants encourage the colleges to partner with other colleges, K-12 schools, community-based organizations, businesses and entrepreneurs. If you are a producer or entrepreneur, or have other interest in the development of renewable energy through agriculture in Eastern and Central Montana, please contact Miles Community College (1-800-541-9281) or Dawson Community College (1-800-821-8320).

An online source of information is the Ethanol Producers And Consumers (EPAC) website at www.ethanolmt.org. EPAC, a national grassroots non-profit organization, is using WIRED grant funds to host educational biofuels workshops around the area.

ATTACHMENT B

Lifeline, Link-Up & Toll Blocking

Mid-Rivers Communications offers two low-income telephone assistance programs known as Lifeline and Link-Up. Lifeline provides Federal Universal Service support to reduce monthly service charges paid by qualifying low-income customers.

Link-Up provides Federal Universal Service support to reduce service connection and line extension charges paid by qualifying low-income customers.

Mid-Rivers also offers toll blocking. Toll blocking is a service that prevents long distance calling from your telephone.

Please contact your nearest Mid-Rivers customer service office or call Mid-Rivers at 1-800-452-2288 for further information.

773-5893

MID-RIVERS 55th Annual Meeting

Wednesday, May 30, 2007

Circle

Business Meeting begins at 1 p.m.

Lunch served starting at

11 a.m. in the Schmidt's Banquet

Room in Circle.


Attendance Gift

Door Prizes

Savings Bond Prize

Cash Prize (Must be present to win)

Don't miss your chance to participate in your cooperative's business...VOTE!

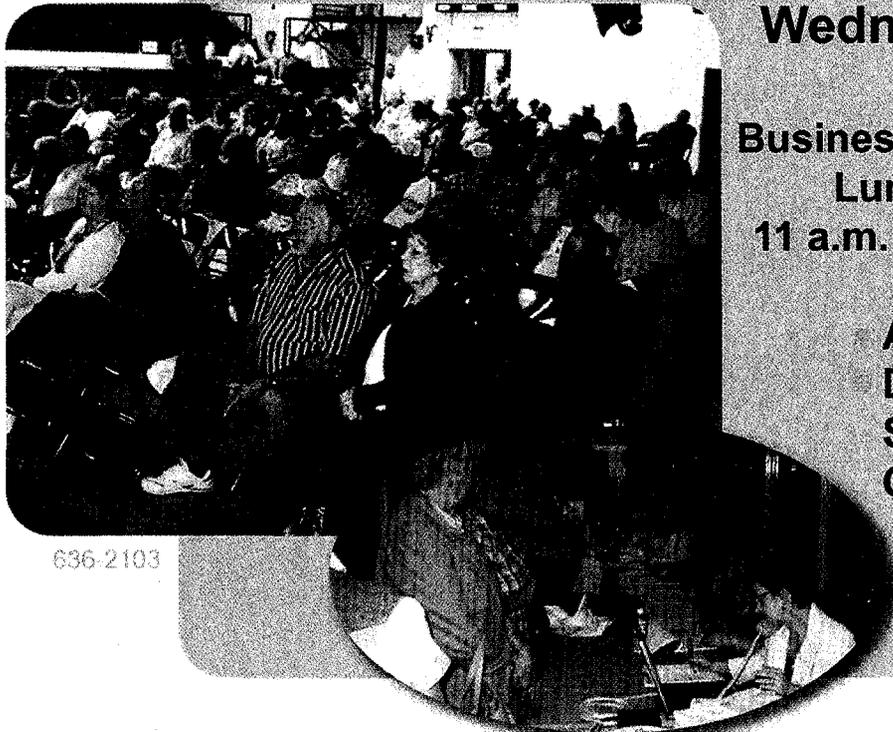

636-2103



Radio

Telephone Number Prize

Ten telephone numbers of Mid-Rivers Telephone Cooperative members are listed throughout this issue of "411." If one of these phone numbers is yours, you are eligible for a \$10 credit applied to your next Mid-Rivers bill. To get this \$10 credit, call Mid-Rivers at 1-800-452-2288.

Page 3

March/April Issue 2007

ATTACHMENT C

Updated 5-Year Build-Out Plan

Cable & Communications Corporation

d/b/a

Mid-Rivers Cellular

- a. **2005 Plan** (in addition to the Digital Upgrade, which was **completed on November 11, 2005**):
 - i. Hammond cell site (45-12-13.4N / 104-55-33.1W)- **completed November 11, 2005**
 - ii. Baker II cell site (46-22-5.4N / 104-16-30.2W)- **completed November 11, 2005**
 - iii. Broadus II cell extender (45-26-55N / 105-24-38W)- **completed January 26, 2006**
 - iv. Ismay cell extender (46-24-05.0N / 104-48-09.0W)- **completed January 26, 2006**

- b. **2006 Plan:**
 - i. Vida South cell site (47-44-14.8N / 105-29-42.0W)- **completed December 22, 2006**
 - ii. North Lambert cell site (47-47-52.9N / 104-38-13.0W) – **completed December 30, 2006**
 - iii. Richey cell extender (47-38-38.3N / 105-04-6.4W) – **completed January 23, 2007**

- c. **2007 Plan:**
 - i. Grass Range cell site (47-01-37N / 108-48-12W) – **completed April 25, 2007**
 - ii. Roy cell site (47-20-04.15N / 108-57-28.91W) – **completed April 25, 2007**
 - iii. Savage cell site (47-27-10.6N / 104-20-19.7W) – **site acquisition in progress**
 - iv. Alzada cell site (45-03-29.8N / 104-27-9.2W) – **construction in process**
 - v. Volborg cell site (45-57-15.97N / 105-38-22.98W) – **site preparation and construction in progress**
 - vi. Sheep Mountain cell site (47-3-5.3N / 105-43-38.8W) – **site acquisition in progress**
 - vii. Ismay CDMA upgrade (46-24-05.0N / 104-48-09.0W) -- **specifying equipment**

- d. **2008 Plan:**
 - i. Rock Springs digital upgrade – **equipment specs in process**

- ii. Weldon cell site (47-39-50.5N / 105-56-35W) -exploring site location
- iii. Otter Creek cell site (45-21-39.8N / 105-50-27.8W) - exploring site location
- iv. Cohagen cell site (47-02-49N / 106-40-52W) -exploring site location

e. 2009 Plan:

- i. Highway 201 West cell site (47-41-01.02N / 104-37-13.05W)-exploring site location
- ii. Highway 59 North cell site (46-11-32.41N / 105-39-04.19W)-exploring site location
- iii. Ashland West cell extender (45-37-38N / 106-30-23.2W)-exploring site location

ATTACHMENT D **Mid-Rivers**

C E L L U L A R

P.O. Box 280 • 904 C Avenue
 Circle, Montana 59215
 (406) 485-3301 • Fax: (406) 485-2924
www.midrivers.com

March 20, 2007

CERTIFIED MAIL/
RETURN RECEIPT REQUESTED

Jace Killstack
 Northern Cheyenne Tribal Council
 PO Box 128
 Lame Deer, MT 59043

RE: Proposed Wireless Site

Jace:

Mid-Rivers Cellular wishes to again extend its offer to serve the Northern Cheyenne area with wireless services. If we can be of any help in providing additional information or answering any questions, please feel free to contact Becky Schmidt at 406-687-7326 or James Nash at 406-687-7356.

Thank you.


 Gerry Anderson
 General Manager

SENDER: COMPLETE THIS SECTION	COMPLETE THIS SECTION ON DELIVERY	
<ul style="list-style-type: none"> ■ Complete items 1, 2, and 3. Also complete item 4 if Restricted Delivery is desired. ■ Print your name and address on the reverse so that we can return the card to you. ■ Attach this card to the back of the mailpiece, or on the front if space permits. 	A. Signature <input checked="" type="checkbox"/> <i>Wesley Russett</i>	<input type="checkbox"/> Agent <input type="checkbox"/> Addressee
1. Article Addressed to: Jack Killstack Northern Cheyenne Tribal Council PO Box 128 Lame Deer, MT 59043	B. Received by (Printed Name) <i>Wesley Russett</i>	C. Date of Delivery 3-21-07
2. Article Number (Transfer from sender)	D. Is delivery address different from item 1? <input type="checkbox"/> Yes If YES, enter delivery address below: <input type="checkbox"/> No	
3. Service Type <input checked="" type="checkbox"/> Certified Mail <input type="checkbox"/> Express Mail <input type="checkbox"/> Registered <input checked="" type="checkbox"/> Return Receipt for Merchandise <input type="checkbox"/> Insured Mail <input type="checkbox"/> C.O.D.		
4. Restricted Delivery? (Extra Fee) <input type="checkbox"/> Yes		
Article Number: 7004 2890 0003 4119 0549		

ATTACHMENT E
PROGRESS REPORT
ALZADA CELL SITE

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	5/2004
Preliminary Engineering	5/2004
Preliminary Environmental Review	7/2007
Preliminary Cultural Impact Review	7/2007
Preliminary Historical Impact Review	7/2007
Preliminary Geophysical Review	7/2007
Real Property - Site Procurement	
Ownership Report from Title Company	4/2006
Discussions with Landowner	4/2006
Documentation of site use arrangements	5/2006
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	6/2006
Federal Communications Commission (FCC)	
Antenna Structure Registration	N/A
Attorney to file cellular Phase II Application w/FCC	7/17/2006
FCC Public Notice -- cellular	7/26/2006
FCC approval notice -- cellular	2/27/2007
Cellular license issued by FCC	2/27/2007
Site interconnection arrangements	4/30/2007
If microwave coordination:	
Attorney to file microwave application w/FCC	3/6/2007
FCC Public Notice -- microwave	3/7/2007
FCC approval notice -- microwave	4/17/2007
Microwave license issued by FCC	4/17/2007
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	6/28/2006
Submit cellular radio installation specifications & contract to contractors for quotes	6/28/2006
Finalize cellular contract	7/6/2006
Contractor to install cellular radio	
Prepare microwave radio installation specifications & contract	6/1/2006
Submit microwave radio installation specifications & contract to contractors for quotes	6/30/2006
Finalize microwave contract	6/15/2007
Contractor to install microwave radio	6/27/2007
Prepare misc. equipment, hardware and power plant specifications	9/13/2006
Purchase misc. equipment, hardware and power plant	10/5/2006
Delivery of misc. equipment, hardware and power plant	6/6/2007
MRC personnel to install misc. equipment, hardware and power plant	6/20/2007

ATTACHMENT E
PROGRESS REPORT
ALZADA CELL SITE

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	7/26/2006
Foundation & gen. slab installation by MRC personnel	5/29/2007
Prepare building specifications & contract	8/9/2006
Submit building specifications & contract to contractors for quotes	N/A
Finalize contract to purchase building	N/A
Building delivery to MRC Supply	N/A
Quotes for Offloading Building	8/1/2006
Offload Building	6/5/2007
Rekey Building	N/A
Quotes for MRTC Sign	N/A
MRTC Sign Installation	7/31/2007
Site development & landscaping by MRC personnel	7/31/2007
Provide building information to COE/Network Engineer for inclusion in company database	4/18/2007
Tower	
Obtain structural analysis of existing tower, if any	N/A
Prepare tower and antenna specifications & contract	6/1/2006
Submit tower and antenna specifications & contract to contractors w/request for quotes	6/21/2006
Finalize contract	4/1/2007
Contractor to complete contract & install tower and antenna(s)	6/8/2007
Contractor to post antenna structure registration number on tower	6/8/2007
Generator	
Purchase Generator, ATS	6/29/2006
Delivery of Generator, ATS	6/5/2007
Test & Turn-up Generator	6/8/2007
Provide generator information to COE/Network Engineer for inclusion in company database	4/18/2007
Power	
Provide local power utility company information on electrical line required	8/8/2006
Power utility company Install electrical lines	5/2/2007
Provide local power utility company information on gas line requirements	N/A
Power utility company install gas lines	N/A
Misc. Electrical Contract	
Quotes for Misc. Electrical	8/11/2006
Award Contract	4/1/2007
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	5/22/2007
Contractor to Provide Warranty Info on Installed Equipment	4/1/2007
Estimated Completion Date	
	7/31/2007

ATTACHMENT F
PROGRESS REPORT
VOLBORG CELL SITE

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	1/17/2007
Preliminary Engineering	6/1/2007
Preliminary Environmental Review	7/6/2007
Preliminary Cultural Impact Review	7/6/2007
Preliminary Historical Impact Review	7/6/2007
Preliminary Geophysical Review	7/6/2007
Real Property - Site Procurement	
Ownership Report from Title Company	9/2002
Discussions with Landowner	5/2007
Documentation of site use arrangements	6/2007
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	7/2007
Federal Communications Commission (FCC)	
Antenna Structure Registration	7/2007
Attorney to file cellular Phase II Application w/FCC	7/2007
FCC Public Notice -- cellular	7/2007
FCC approval notice -- cellular	8/2007
Cellular license issued by FCC	9/2007
Site interconnection arrangements	7/2007
If microwave coordination:	
Attorney to file microwave application w/FCC	7/2007
FCC Public Notice -- microwave	7/2007
FCC approval notice -- microwave	8/2007
Microwave license issued by FCC	9/2007
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	5/18/2007
Submit cellular radio installation specifications & contract to contractors for quotes	6/7/2007
Finalize cellular contract	6/7/2007
Contractor to install cellular radio	9/21/2007
Prepare microwave radio installation specifications & contract	5/31/2007
Submit microwave radio installation specifications & contract to contractors for quotes	5/15/2007
Finalize microwave contract	7/13/2007
Contractor to install microwave radio	9/14/2007
Prepare misc. equipment, hardware and power plant specifications	7/31/2007
Purchase misc. equipment, hardware and power plant	6/8/2007
Delivery of misc. equipment, hardware and power plant	8/17/2007
MRC personnel to install misc. equipment, hardware and power plant	9/21/2007

ATTACHMENT F
PROGRESS REPORT
VOLBORG CELL SITE

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	
Foundation & gen. slab installation by MRC personnel	8/31/2007
Prepare building specifications & contract	N/A
Submit building specifications & contract to contractors for quotes	N/A
Finalize contract to purchase building	N/A
Building delivery to MRC Supply	IN SUPPLY
Quotes for Offloading Building	7/6/2007
Offload Building	8/31/2007
Rekey Building	8/31/2007
Quotes for MRTC Sign	7/30/2007
MRTC Sign Installation	10/1/2007
Site development & landscaping by MRC personnel	10/1/2007
Provide building information to COE/Network Engineer for inclusion in company database	10/7/2007
Tower	
Obtain structural analysis of existing tower, if any	N/A
Prepare tower and antenna specifications & contract	6/13/2007
Submit tower and antenna specifications & contract to contractors w/request for quotes	6/15/2007
Finalize contract	7/6/2006
Contractor to complete contract & install tower and antenna(s)	9/21/2007
Contractor to post antenna structure registration number on tower	9/21/2007
Generator	
Purchase Generator, ATS	6/8/2007
Delivery of Generator, ATS	9/7/2007
Test & Turn-up Generator	9/7/2007
Provide generator information to COE/Network Engineer for inclusion in company database	10/1/2007
Power	
Provide local power utility company information on electrical line required	5/21/2007
Power utility company Install electrical lines	6/1/2007
Provide local power utility company information on gas line requirements	N/A
Power utility company install gas lines	N/A
Misc. Electrical Contract	
Quotes for Misc. Electrical	5/15/2007
Award Contract	7/30/2007
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	8/3/2007
Contractor to Provide Warranty Info on Installed Equipment	8/17/2007
Estimated Completion Date	10/30/2007

ATTACHMENT G
PROGRESS REPORT
SHEEP MOUNTAIN CELL SITE

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	1/18/2007
Preliminary Engineering	6/8/2007
Preliminary Environmental Review	6/15/2007
Preliminary Cultural Impact Review	6/15/2007
Preliminary Historical Impact Review	6/15/2007
Preliminary Geophysical Review	6/15/2007
Real Property - Site Procurement	
Ownership Report from Title Company	7/2007
Discussions with Landowner	6/2007
Documentation of site use arrangements	6/2007
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	7/2007
Federal Communications Commission (FCC)	
Antenna Structure Registration	9/2007
Attorney to file cellular Phase II Application w/FCC	9/2007
FCC Public Notice -- cellular	9/2007
FCC approval notice -- cellular	11/2007
Cellular license issued by FCC	11/2007
Site interconnection arrangements	N/A
If microwave coordination:	N/A
Attorney to file microwave application w/FCC	8/1/2007
FCC Public Notice -- microwave	8/1/2007
FCC approval notice -- microwave	9/1/2007
Microwave license issued by FCC	10/1/2007
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	5/18/2007
Submit cellular radio installation specifications & contract to contractors for quotes	6/7/2007
Finalize cellular contract	6/7/2007
Contractor to install cellular radio	
Prepare microwave radio installation specifications & contract	5/31/2007
Submit microwave radio installation specifications & contract to contractors for quotes	5/15/2007
Finalize microwave contract	7/13/2007
Contractor to install microwave radio	
Prepare misc. equipment, hardware and power plant specifications	6/27/2007
Purchase misc. equipment, hardware and power plant	7/3/2007
Delivery of misc. equipment, hardware and power plant	8/10/2007
MRC personnel to install misc. equipment, hardware and power plant	9/28/2007

ATTACHMENT G
PROGRESS REPORT
SHEEP MOUNTAIN CELL SITE

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	7/20/2007
Foundation & gen. slab installation by MRC personnel	8/3/2007
Prepare building specifications & contract	In Supply
Submit building specifications & contract to contractors for quotes	NA
Finalize contract to purchase building	NA
Building delivery to MRC Supply	In Supply
Quotes for Offloading Building	8/3/2007
Offload Building	8/10/2007
Rekey Building	7/20/2007
Quotes for MRTC Sign	7/20/2007
MRTC Sign Installation	11/2/2007
Site development & landscaping by MRC personnel	11/30/2007
Provide building information to COE/Network Engineer for inclusion in company database	11/30/2007
Tower	
Obtain structural analysis of existing tower, if any	
Prepare tower and antenna specifications & contract	6/13/2007
Submit tower and antenna specifications & contract to contractors w/request for quotes	6/15/2007
Finalize contract	7/2/2007
Contractor to complete contract & install tower and antenna(s)	10/12/2007
Contractor to post antenna structure registration number on tower	11/30/2007
Generator	
Purchase Generator, ATS	8/1/2007
Delivery of Generator, ATS	8/24/2007
Test & Turn-up Generator	8/31/2007
Provide generator information to COE/Network Engineer for inclusion in company database	11/30/2007
Power	
Provide local power utility company information on electrical line required	6/15/2007
Power utility company Install electrical lines	8/3/2007
Provide local power utility company information on gas line requirements	8/31/2007
Power utility company install gas lines	8/17/2007
Misc. Electrical Contract	
Quotes for Misc. Electrical	7/2/2007
Award Contract	7/13/2007
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	7/20/2007
Contractor to Provide Warranty Info on Installed Equipment	11/30/2007
Estimated Completion Date	
	11/30/2007

ATTACHMENT H
PROGRESS REPORT
ISMAY CDMA SITE UPGRADE

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	in place
Preliminary Engineering	in place
Preliminary Environmental Review	in place
Preliminary Cultural Impact Review	in place
Preliminary Historical Impact Review	in place
Preliminary Geophysical Review	in place
Real Property - Site Procurement	
Ownership Report from Title Company	in place
Discussions with Landowner	in place
Documentation of site use arrangements	in place
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	EXISTING
Federal Communications Commission (FCC)	
Antenna Structure Registration	N/A
Attorney to file cellular Phase II Application w/FCC	9/2007
FCC Public Notice -- cellular	9/2007
FCC approval notice -- cellular	11/2007
Cellular license issued by FCC	11/2007
Site interconnection arrangements	N/A
If microwave coordination:	n/a
Attorney to file microwave application w/FCC	n/a
FCC Public Notice -- microwave	n/a
FCC approval notice -- microwave	n/a
Microwave license issued by FCC	n/a
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	5/18/2007
Submit cellular radio installation specifications & contract to contractors for quotes	6/7/2007
Finalize cellular contract	6/7/2007
Contractor to install cellular radio	11/16/2007
Prepare microwave radio installation specifications & contract	n/a
Submit microwave radio installation specifications & contract to contractors for quotes	n/a
Finalize microwave contract	n/a
Contractor to install microwave radio	n/a
Prepare misc. equipment, hardware and power plant specifications	9/7/2007
Purchase misc. equipment, hardware and power plant	9/14/2007
Delivery of misc. equipment, hardware and power plant	10/19/2007
MRC personnel to install misc. equipment, hardware and power plant	11/16/2007

ATTACHMENT H
PROGRESS REPORT
ISMAY CDMA SITE UPGRADE

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	8/17/2007
Foundation & gen. slab installation by MRC personnel	9/14/2007
Prepare building specifications & contract	8/17/2007
Submit building specifications & contract to contractors for quotes	8/17/2007
Finalize contract to purchase building	8/24/2007
Building delivery to MRC Supply	9/21/2007
Quotes for Offloading Building	8/17/2007
Offload Building	10/5/2007
Rekey Building	11/1/2007
Quotes for MRTC Sign	8/10/2007
MRTC Sign Installation	11/1/2007
Site development & landscaping by MRC personnel	12/31/07
Provide building information to COE/Network Engineer for inclusion in company database	12/31/2007
Tower	
Obtain structural analysis of existing tower, if any	n/a
Prepare tower and antenna specifications & contract	n/a
Submit tower and antenna specifications & contract to contractors w/request for quotes	n/a
Finalize contract	n/a
Contractor to complete contract & install tower and antenna(s)	n/a
Contractor to post antenna structure registration number on tower	n/a
Generator	
Purchase Generator, ATS	9/7/2007
Delivery of Generator, ATS	10/12/2007
Test & Turn-up Generator	10/26/2007
Provide generator information to COE/Network Engineer for inclusion in company database	11/2/2007
Power	
Provide local power utility company information on electrical line required	in place
Power utility company Install electrical lines	in place
Provide local power utility company information on gas line requirements	n/a
Power utility company install gas lines	n/a
Misc. Electrical Contract	
Quotes for Misc. Electrical	9/7/2007
Award Contract	9/10/2007
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	9/14/2007
Contractor to Provide Warranty Info on Installed Equipment	12/31/2007
Estimated Completion Date	

ATTACHMENT I
PROGRESS REPORT
SAVAGE CELL SITE

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	5/24/2007
Preliminary Engineering	5/24/2007
Preliminary Environmental Review	EXISTING
Preliminary Cultural Impact Review	EXISTING
Preliminary Historical Impact Review	EXISTING
Preliminary Geophysical Review	EXISTING
Real Property - Site Procurement	
Ownership Report from Title Company	EXISTING
Discussions with Landowner	EXISTING
Documentation of site use arrangements	EXISTING
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	7/2007
Federal Communications Commission (FCC)	
Antenna Structure Registration	N/A
Attorney to file cellular Phase II Application w/FCC	9/2007
FCC Public Notice -- cellular	9/2007
FCC approval notice -- cellular	11/2007
Cellular license issued by FCC	11/2007
Site interconnection arrangements	N/A
If microwave coordination:	N/A
Attorney to file microwave application w/FCC	N/A
FCC Public Notice -- microwave	N/A
FCC approval notice -- microwave	N/A
Microwave license issued by FCC	N/A
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	5/18/2007
Submit cellular radio installation specifications & contract to contractors for quotes	6/7/2007
Finalize cellular contract	6/7/2007
Contractor to install cellular radio	10/5/2007
Prepare microwave radio installation specifications & contract	N/A
Submit microwave radio installation specifications & contract to contractors for quotes	N/A
Finalize microwave contract	N/A
Contractor to install microwave radio	N/A
Prepare misc. equipment, hardware and power plant specifications	9/14/2007
Purchase misc. equipment, hardware and power plant	8/24/2007
Delivery of misc. equipment, hardware and power plant	9/21/2007
MRC personnel to install misc. equipment, hardware and power plant	10/5/2007

ATTACHMENT I
PROGRESS REPORT
SAVAGE CELL SITE

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	EXISTING
Foundation & gen. slab installation by MRC personnel	NA
Prepare building specifications & contract	NA
Submit building specifications & contract to contractors for quotes	NA
Finalize contract to purchase building	NA
Building delivery to MRC Supply	NA
Quotes for Offloading Building	NA
Offload Building	NA
Rekey Building	NA
Quotes for MRTC Sign	NA
MRTC Sign Installation	NA
Site development & landscaping by MRC personnel	11/15/2007
Provide building information to COE/Network Engineer for inclusion in company database	11/15/2007
Tower	
Obtain structural analysis of existing tower, if any	N/A
Prepare tower and antenna specifications & contract	6/14/2007
Submit tower and antenna specifications & contract to contractors w/request for quotes	6/15/2007
Finalize contract	6/29/2007
Contractor to complete contract & install tower and antenna(s)	9/21/2005
Contractor to post antenna structure registration number on tower	10/26/2007
Generator	
Purchase Generator, ATS	NA
Delivery of Generator, ATS	NA
Test & Turn-up Generator	NA
Provide generator information to COE/Network Engineer for inclusion in company database	NA
Power	
Provide local power utility company information on electrical line required	EXISTING
Power utility company Install electrical lines	NA
Provide local power utility company information on gas line requirements	NA
Power utility company install gas lines	NA
Misc. Electrical Contract	
Quotes for Misc. Electrical	9/7/2007
Award Contract	9/14/2007
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	9/17/2007
Contractor to Provide Warranty Info on Installed Equipment	9/21/2007
Estimated Completion Date	11/15/2007

Mid-Rivers NEW Cellular Plans




Cellular
Plans
to fit
your
lifestyle!

Mid-Rivers

C E L L U L A R

1-800-452-2288 or visit our
website at www.midrivers.com

ATTACHMENT J

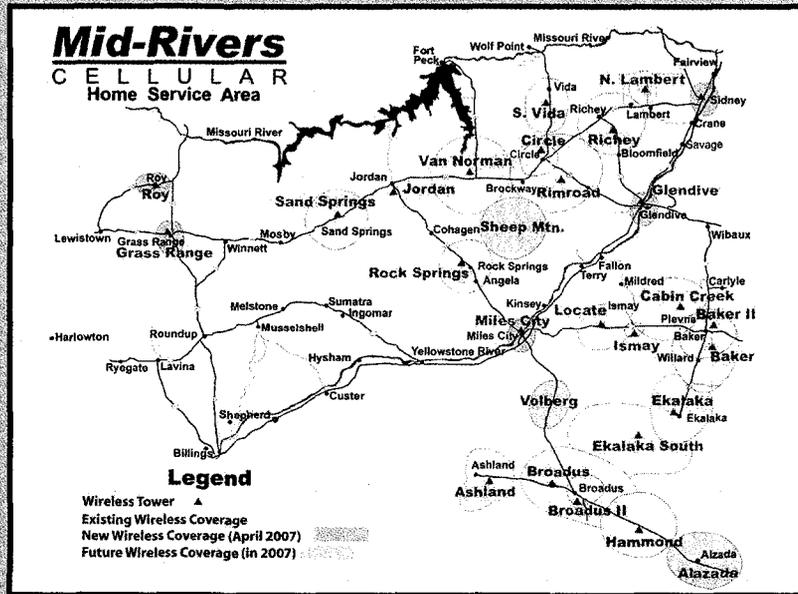

Additional Phone Plateaus	
A *	
Total of 4 Phones	\$9.95
5-19 Phones	\$8.95
20-29 Phones	\$7.95
30 and over	\$4.95
B **	
Total of 5 Phones	\$9.95
6 or more Phones	\$20.00

Freedom West Plan:
Freedom West allows the customer to call from a Mid-Rivers cellular tower to Montana, North Dakota, South Dakota and Wyoming toll free. Airtime minutes still are used.

Text Messaging		
\$2.99/mo.	50 messages	Total incoming & outgoing
\$4.99/mo.	200 messages	Total incoming & outgoing
\$9.99/mo.	1000 messages	Total incoming & outgoing
\$19.99/mo.	Unlimited messages	Both incoming & outgoing

Pay-per use messaging is \$0.07 per message for incoming & outgoing. Text messaging must be activated on digital cell phones.

Mobile Internet Plans:	
\$6.99/mo.	2-Meg of data (\$0.02/KB over 2-Meg)
\$59.99/mo.	Unlimited
Start-Up Promo of \$49.99/mo. \$15 Activation Fee waived during Start-Up Promo	
Equipment:	
\$99.99 with 2-yr contract or \$219.99 with 1-yr contract on Kyocera Data Card. OR	
\$59.99 with 1-yr contract for Data Kit connecting laptop while using cell phone as a modem.	

Cellular Value Plans	Monthly Charge	Additional Phone Plateau *	Anywhere Minutes	Airtime Overage Per Minute	Nation Wide Long Distance on Home Tower	Long Distance Roaming Rate	Freedom West	Calling Features	Caller ID	Voice Mail
Security	\$19.95	A	100	0.35	0.15/min	Charges Vary	FREE	3.95	3.00	3.95
Family	\$29.95	A	250	0.35	0.15/min	Charges Vary	FREE	3.95	3.00	3.95
Plainsman	\$36.95	A	350	0.35	0.15/min	Charges Vary	FREE	3.95	3.00	3.95

Cellular Value Added Plans	Monthly Charge	Anywhere Roaming Minutes	Roaming Airtime Overage Per Minute	Anytime Home Minutes	Additional Phone Plateau **	Nation Wide Long Distance on Home Tower	Nation Wide Roaming Long Distance	Long Distance Roaming Rate	Calling Features and Caller ID	Voice Mail
Rancher	\$44.95	400	0.35	Unlimited	B	Unlimited	100 FREE minutes - overage charges may vary	Charges Vary	Free	3.95
Pioneer	\$69.95	600	0.35	Unlimited	B	Unlimited	125 FREE minutes - overage charges may vary	Charges Vary	Free	3.95
Powder River	\$89.95	800	0.35	Unlimited	B	Unlimited	150 FREE minutes - overage charges may vary	Charges Vary	Free	3.95
Traveler	\$109.95	1000	0.35	Unlimited	B	Unlimited	175 FREE minutes - overage charges may vary	Charges Vary	Free	3.95
Badlands	\$139.95	1300	0.35	Unlimited	B	Unlimited	200 FREE minutes - overage charges may vary	Charges Vary	Free	3.95
Yellowstone	\$159.95	1500	0.35	Unlimited	B	Unlimited	225 FREE minutes - overage charges may vary	Charges Vary	Free	3.95
