

CABLE & COMMUNICATIONS CORPORATION

Box 106 MASTER FILE

904 C Avenue
P.O. Box 280
Circle, Montana 59215
Ph: (406) 485-3301

2008 JUN 30

June 27, 2008

VIA UPS NEXT DAY AIR
1Z 597 675 22 1000 256 6

Kate Whitney
Montana Public Service Commission
1701 Prospect Avenue
Helena, MT 59620-2601

RE: Cable & Communications Corporation dba Mid-Rivers Cellular
Twelfth Quarterly and Sixth Semi-Annual Report as Required
By Final Order 6518a
Docket No. D2003.8.105

Ms. Whitney:

Enclosed for filing are an original and ten (10) copies of Cable & Communications Corporation dba Mid-Rivers Cellular's Twelfth Quarterly and Sixth Semi-Annual Report as Required by Final Order 6518a in the above-referenced docket. Also enclosed is a disk with an electronic (pdf/Adobe Acrobat) copy of the document.

Feel free to contact me if you have any questions.

Thank you.


Gerry Anderson
General Manager

Enclosures

RECEIVED BY
MONTANA PUBLIC SERVICE COMMISSION
JUN 30 10 31 AM '08

DISK RCVD

RECEIVED BY
2008 JUN 30 A 10:32
PUBLIC SERVICE
COMMISSION

DEPARTMENT OF PUBLIC SERVICE REGULATION
BEFORE THE PUBLIC SERVICE COMMISSION
OF THE STATE OF MONTANA

IN THE MATTER OF THE PETITION OF)	UTILITY DIVISION
CABLE & COMMUNICATIONS)	
CORPORATION, dba MID-RIVERS)	DOCKET NO. D2003.8.105
CELLULAR, for Designation as an Eligible)	
Telecommunications Carrier)	

CABLE & COMMUNICATIONS CORPORATION,
dba MID-RIVERS CELLULAR'S
TWELFTH QUARTERLY AND SIXTH SEMI-ANNUAL REPORT
AS REQUIRED BY FINAL ORDER DATED MARCH 29, 2005
(PSC Order No. 6518a)

Service Date: June 27, 2008

TWELFTH QUARTERLY REPORT

- I. Unsatisfied Requests – March 16 through June 15, 2008:
 - a. By location in each of the two study areas:
 - i. Mid-Rivers Study Area: zero (0).
 - ii. Range Study Area: zero (0).
 - b. Detailed description of why customer requests for service could not be satisfied: there were no unsatisfied requests.

- II. Customer Complaints – March 16 through June 15, 2008:
 - a. Number and nature of complaints: see Attachment A hereto.
 - b. Remedy employed to address complaints: see Attachment A hereto.
 - c. Location of complaints by Study Area:
 - i. Mid-Rivers: see Attachment A hereto.
 - ii. Range: see Attachment A hereto.
 - d. Number of repeat complaints: see Attachment A hereto.

- III. Federal Universal Service Funds, including Lifeline and Link Up Funds received – March 16 through June 15, 2008:
 - a. Funds received:
 - i. Interstate Common Line Support:
 - 1. \$37,070.00 received in April 2008 for February 2008.
 - 2. \$37,070.00 received in May 2008 for March 2008.
 - 3. \$37,964.00 received in June 2008 for April 2008.

ii. High Cost Loop Support:

1. \$47,415.00 received in April 2008 for February 2008.
2. \$47,415.00 received in May 2008 for March 2008.
3. \$48,126.00 received in June 2008 for April 2008.

iii. Local Switching Support:

1. \$7,034.00 received in April 2008 for February 2008.
2. \$7,034.00 received in May 2008 for March 2008.
3. (\$9,737.00) received in June 2008 for April 2008.

iv. Lifeline and Link Up Funds:

1. \$0 received to date.

SIXTH SEMI-ANNUAL REPORT

- IV. 5-Year Build-out Plan, updated for the period of December 16, 2007, through June 15, 2008: see Attachment B hereto.
- a. Including expanded coverage in Northern Cheyenne Reservation, unless conflicting licenses, in which case an explanation of those conflicts must be provided:
- i. Representatives from Cable & Communications Corporation conducted an on-site meeting with Jace Killsback at the Northern Cheyenne Tribal Council in Lame Deer, Montana, on February 17, 2006.
 - ii. Letters addressed to Jace Killsback of the Northern Cheyenne Reservation dated May 15, 2006, and June 16, 2006, were filed with the Commission in Cable & Communications Corporation's Second Semi-Annual Report of June 27, 2006. No response has been received to date.
 - iii. A letter addressed to Jace Killsback of the Northern Cheyenne Reservation dated March 20, 2007, was mailed via certified mail/return receipt requested and was signed in receipt on March 21, 2007. This letter was filed with the Commission in Cable & Communications Corporation's Eighth Quarterly and Fourth Semi-Annual Report of June 29, 2007.
 - iv. Representatives from Cable & Communications Corporation conducted a meeting with Danny Sioux, Rosebud County

Commissioner and member of the Northern Cheyenne Tribe, in Miles City, Montana, on September 11, 2007.

- v. See Attachment C hereto, which is a letter addressed to Geri Small, President, of the Northern Cheyenne Reservation mailed March 31, 2008, documenting C&CC's continuing attempts to establish cellular services on the Northern Cheyenne Reservation.

V. Updated population coverage estimates are provided based on the 5-Year Build-out Plan. The information provided is based on January 1, 2007, population estimates. See Attachment D hereto.

VI. Reports on Progress in expanding wireless coverage. Reports are provided for those sites on which work has been commenced.

- a. Plevna: see Attachment E hereto.
- b. Lambert 2-Way: see Attachment F hereto.
- c. McGuire Creek: see Attachment G hereto.
- d. Otter Creek: see Attachment H hereto.
- e. North Cohagen: see Attachment I hereto.

Attachment A

Mid-Rivers Cellular Quarterly Trouble Report


March 16, 2008 - June 15, 2008

19 - Total Cellular inquiries/troubles logged

6 - Alarms and troubles reported by other carrier's customers

13 - Troubles reported by Mid-Rivers Cellular Customers

Cellular Exchanges	Cellular Troubles	Out of Service	Repeat Troubles
<i>Range Study Area</i>			
(406) 983 Ashland	0	0	0
(406) 938 Alzada	0	0	0
(406) 935 Broadus	1	0	0
(406) 981 South Miles City	0	0	0
<i>Mid-Rivers Study Area</i>			
(406) 978 Baker	6	0	0
(406) 974 Circle	2	0	0
(406) 975 Ekalaka	0	0	0
(406) 977 Jordan	4	0	0
(406) 914 Lambert	0	0	0
(406) 971 Plevna	0	0	0
(406) 979 Richey	0	0	0
(406) 928 Grass Range	0	0	0
(406) 915 South Wolf Point	0	0	0
(406) 954 Roy	0	0	0
Total	13	0	0

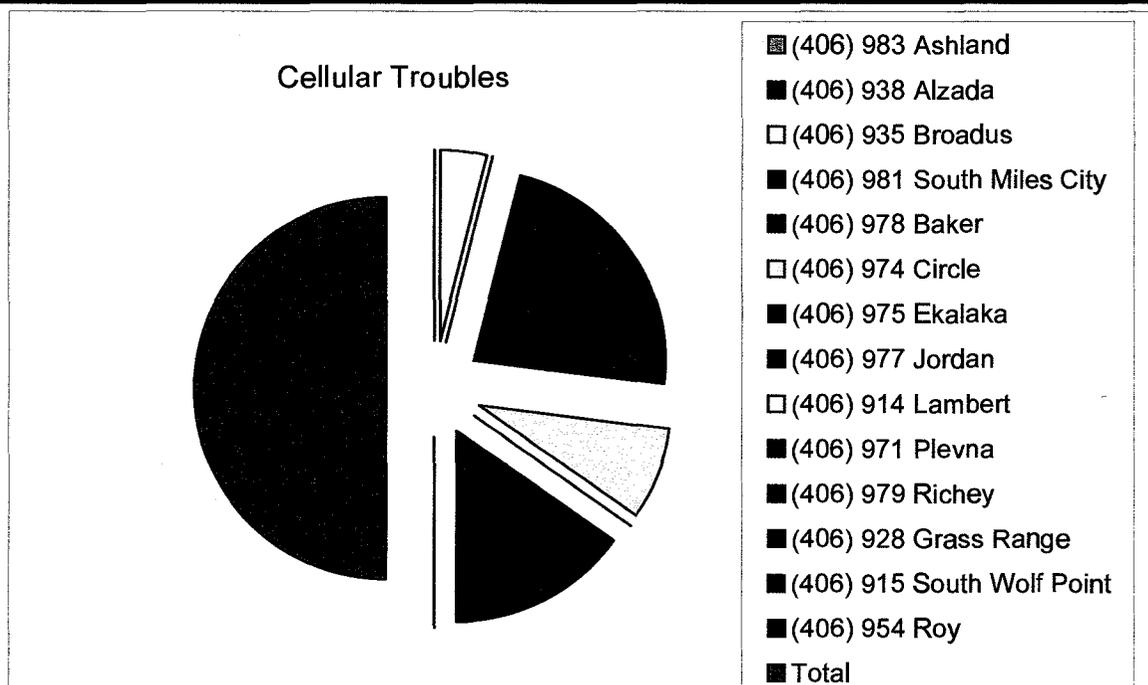

Repair Time for Cellular Troubles	24 hours	48 hours	72 hours
Number of troubles repaired	9	11	12
Total in Percentages	69%	85%	92%

69% of troubles were dispatched and repaired within 24 hours. 4 remaining troubles were cleared outside the 24 hour period. These 4 troubles all required education of the customer and/or the activation of a new or different cell phone.

2,775 - Total Mid-Rivers Cellular Customers

.47 Trouble Index for Mid-River's Cellular Customers (per 100 customers)

ATTACHMENT B

Updated 5-Year Build-Out Plan

Cable & Communications Corporation

d/b/a

Mid-Rivers Cellular


- a. **2005 Plan** (in addition to the Digital Upgrade, which was completed on **November 11, 2005**):
 - i. Hammond (45-12-13.4N / 104-55-33.1W)-**completed November 11, 2005**
 - ii. Baker II (46-22-5.4N / 104-16-30.2W)- **completed November 11, 2005**
 - iii. Broadus II (45-26-55N / 105-24-38W)- **completed January 26, 2006**
 - iv. Ismay (46-24-05.0N / 104-48-09.0W)- **completed January 26, 2006**

- b. **2006 Plan:**
 - i. Vida South (47-44-14.8N / 105-29-42.0W)- **completed December 22, 2006**
 - ii. North Lambert (47-47-52.9N / 104-38-13.0W) –**completed December 30, 2006**
 - iii. Richey (47-38-38.3N / 105-04-6.4W) –**completed January 23, 2007**

- c. **2007 Plan:**
 - i. Grass Range (47-01-37N / 108-48-12W) –**completed April 25, 2007**
 - ii. Roy (47-20-04.15N / 108-57-28.91W) –**completed April 25, 2007**
 - iii. Savage (47-27-10.6N / 104-20-19.7W) – **completed November 19, 2007**
 - iii. Alzada (45-03-29.8N / 104-27-9.2W) – **completed July 13, 2007**
 - iv. Volborg (45-57-15.97N / 105-38-22.98W) –**completed December 7, 2007**
 - v. Sheep Mountain (47-3-5.3N / 105-43-38.8W) –**completed December 7, 2007**
 - vi. Winnett (46-59-21.0N / 108-20-02.0W) – **completed December 10, 2007**
 - vii. Rock Springs – **completed December 7, 2007**

- d. **2008 Plan:**
- i. Plevna (46-27-12.9N / 104-30-42.6W) –**working with landowner**
 - ii. Lambert 2-Way (47-36-02N / 104-35-00W) – **reviewing licensing options**
 - iii. McGuire Creek (47-35-04.75N / 106-09-04.79W) –**working with landowner and preparing site**
 - iv. Otter Creek (45-21-39.8N / 105-50-27.8W) –**exploring site location**
 - v. North Cohagen (47-08-31.7N / 106-43-00.44W) –**working with landowner and preparing site**
- e. **2009 Plan:**
- i. Highway 201 West (47-41-01.02N / 104-37-13.05W)-
exploring site location
 - ii. Highway 59 North (46-11-32.41N / 105-39-04.19W)-
exploring site location
 - iii. Ashland West (45-37-38N / 106-30-23.2W)-exploring site
location
 - iv. Carlyle (46-41-21N / 104-19-44.8W)-exploring site location
 - v. Angela (46-43-45.1N / 106-11-57.0W)-exploring site
location
 - vi. Biddle (45-5-57.9N / 105-20-18.0W)-exploring site location
 - vii. Highway 12 East between Miles City and Locate (46-23-
06N / 105-33-09W)-exploring site location

Even though specific sites are currently scheduled as shown, circumstances such as land availability and licensing issues may cause scheduling changes, e.g., a site currently scheduled for 2009 could be moved to 2008. Also, some of the sites scheduled in 2009 may be constructed earlier if all requirements are fulfilled earlier than projected.



CABLE & COMMUNICATIONS CORPORATION

904 C Avenue
P.O. Box 280
Circle, Montana 59215
Ph: (406) 485-3301

ATTACHMENT C

March 31, 2008

COPY

Geri Small, President
Northern Cheyenne Tribal Council
PO Box 128
Lame Deer, MT 59043

RE: Proposed Wireless Site

President Small:

Mid-Rivers Cellular wishes to again extend its offer to serve the Northern Cheyenne area with wireless services. If we can be of any help in providing additional information or answering any questions, please feel free to contact Becky Schmidt at 406-687-7326 or James Nash at 406-687-7356.

Thank you.


Gerry Anderson
General Manager

BAS/dm

Mid-Rivers Cellular Population Coverage Estimates
Based on Jan. 1, 2007 Population Estimates

June 18, 2008

Cellular Site	Base Coverage	2006 Plan	2008 Plan	Site Status	Notes*		
	-	-	393	393	393 Completed 7/13/07	24.79 mi radius. 3.9 mi NW of Alzada. License WPSD973.	
	-	-	-	-	357	Exploring site location	25 mi radius. S of Angela, W of Hwy. 59, Rosebud County.
Ashland	775	775	775	775	775	Base coverage	16.4 mi radius. 2 mi E of Ashland. License WPK992.
	-	-	-	-	8,068	Exploring site location	25 mi radius. Between Lane Deer & Ashland on Hwy. 212, N Cheyenne Res.
Baker	2,621	2,621	2,621	2,621	2,621	Base coverage	29.3 mi radius. Approx. 6.9 mi SE of Baker. License KNKR293.
	-	2,621	2,621	2,621	2,621	Completed 11/11/05	19.075 mi radius. 11 E Montana Ave., Baker. License KNKR293.
	-	-	-	-	1,012	Exploring site location	25 mi radius. S of Hwy. 212 on Hwy. 59 at Biddle. Powder River County.
Broadus	1,575	1,575	1,575	1,575	1,575	Base coverage	30.05 mi radius. N of Hwy 212, 5 mi WNW of Broadus. License WPSD973.
	-	1,272	1,272	1,272	1,272	Completed 1/28/06	19 mi radius. N Broadus. Powder River County.
Cabin Creek	2,777	2,777	2,777	2,777	2,777	Base coverage	29.162 mi radius. Approx. 3.6 mi SW of Cabin Creek. License KNKR293.
	-	-	-	-	3,337	Exploring site location	25 mi radius. W of Hwy. 7 in S Wibaux County.
Circle	1,251	1,251	1,251	1,251	1,251	Base coverage	19.1 mi radius. 904 C Avenue in Circle. License WPZQ261.
Ekalaka	898	898	898	898	898	Base coverage	29.225 mi radius. Approx. .5 mi N of Ekalaka. License KNKR293.
	-	-	-	-	177	Completed 4/25/07	3 mi radius (PCS). 106 E. Fifth Street, Grass Range. License WPZU775.
	-	746	746	746	746	Completed 11/11/05	29.75 mi radius. 2.3 mi S of Hammond on section line road. License WPSD973.
	-	-	-	-	10,986	Exploring site location	25 mi radius. Hwy. 12 E between Miles City and Locate.
	-	-	-	-	8,637	Exploring site location	25 mi radius. S of Hwy. 200 near Lambert in Richland County.
	-	-	-	-	10,392	Exploring site location	25 mi radius. Hwy. 59 S between Miles City and Volborg in Custer County.
	-	1,195	1,195	1,195	1,195	Completed 1/26/06	24.55 mi radius. 181 Ismay RD S, Ismay. License KNKR293.
Jordan	1,145	1,145	1,145	1,145	1,145	Base coverage	21.012 mi radius. Approx. 1.1 mi S of Jordan. License KNKR289.
Lambert	-	-	-	-	8,479	Installing equipment	25 mi radius. W of Sidney on Hwy. 16 in Richland County.
Locate	257	257	257	257	257	Base coverage	19.137 mi radius. 36.6 mi E of Miles City. License KNKR293.
McGuire Creek	-	-	-	-	922	Working w/ landowner	25 mi radius. E of Ft. Peck Dam on Hwy. 24 in McCone County.
North Cohagen	-	-	-	-	780	Exploring site location	25 mi radius. Hwy. 59 N between Jordan and Cohagen in Garfield County.
North Lambert	-	-	1,168	1,168	1,168	Completed 12/30/06	19.95 mi radius. 7.9 mi N of Lambert on CR 328. License KNKR290.
Otter Creek	-	-	-	-	1,222	Exploring site location	25 mi radius. S of Sonnette, S of Hwy. 212 in Powder River County.
Plevna	-	-	-	-	2,641	Working w/ landowner	25 mi radius. N of Plevna on Plevna N Road in Fallon County.
Richey	1,306	1,306	1,306	1,306	1,306	Base coverage	30.688 mi radius. Approx. 7.7 mi SE of Richey. License KNKR290.
Richey II	-	-	333	333	333	Completed 1/23/07	12.09 mi radius. 106 Elk Ave. E in Richey. License KNKR290.
Rim Road	2,109	2,109	2,109	2,109	2,109	Base coverage	28.975 mi radius. 21.76 KM SE of Circle. License KNKR290.
Rock Springs	357	357	357	357	357	Base coverage	24.375 mi radius. 1.5 mi N of Rock Springs. License WPPZ786.
	-	-	-	-	479	Completed 4/25/07	4 mi radius (PCS). 1st Ave., just S of Hwy. 191, Roy. License WPZU775.
Sand Springs	847	847	847	847	847	Base coverage	27.5 mi radius. Approx. 1.6 mi NE of Sand Springs. License KNKR289.
	-	-	-	-	304	Completed 11/19/07	4 mi radius (PCS). 4 blocks E of Hwy. 16, Savage. License WPON362.
	-	-	-	-	2,631	Completed 12/7/07	30.625 mi radius. 26 mi NW of Terry, MT on Sheep Mountain. License KNKR290.
South Ekalaka	2,210	2,210	2,210	2,210	2,210	Base coverage	35.54 mi radius. 27 mi SW of Ekalaka. License WPTV839.
Van Norman	1,251	1,251	1,251	1,251	1,251	Base coverage	29.625 mi radius. 10 mi WNW of Van Norman. License KNKR289.
Vida South	-	-	1,527	1,527	1,527	Completed 12/22/06	24.3 mi radius. 6.5 mi S of Vida on Hwy. 13. License KNKR290.
	-	-	-	-	609	Completed 12/7/07	23.4 mi radius. 6.1 mi N of Volberg on Hwy. 59. License WPTV839.
	-	-	-	-	159	Completed 12/10/07	5 mi radius (PCS). SE of Winnett, S of Hwy. 200. License WPON362.
Adjustments for Overlap	(6,977)	(9,238)	(10,138)	(11,866)	(19,382)	(47,593)	Reduction to account for overlap of populations counted in multiple areas.
TOTALS	12,402	18,103	27,655				


ATTACHMENT D
(Page 1 of 2)

% Change, Base to End 2006	28.81%	3,573	Net Increase in Residents Served
% Change, 2005 to End 2006	13.32%	2,128	Net Increase in Residents Served
% Change, 2006 to End 2007	16.70%	3,024	Net Increase in Residents Served
% Change, 2007 to End 2008	30.90%	6,528	Net Increase in Residents Served
% Change, 2008 to End 2009	52.71%	14,678	Net Increase in Residents Served
% Change, Base to End 2009	240.53%	29,831	Net Increase in Residents Served

*Lat & Long figures used in software application to obtain population information for circular areas were detailed to Degrees, Minutes & Seconds in decimal format to differentiate as much as possible between any closely located towers. Radii for base plan circular calculations based on average distance of signal from SAB according to FCC licensing information. Radii estimated at 25 miles for new cell sites (the average of existing sites). Only Montana populations counted.

Source: MABLE/Geocorr2K: Geographic Correspondence Engine with Census 2000 Geography & Jan. 1, 2007 Estimates. <http://mcdc2.missouri.edu/websas/geocorr2k.html>

Rural Eastern Montanans Receiving Wireless Service Under Mid-Rivers Cellular Build-Out Plan

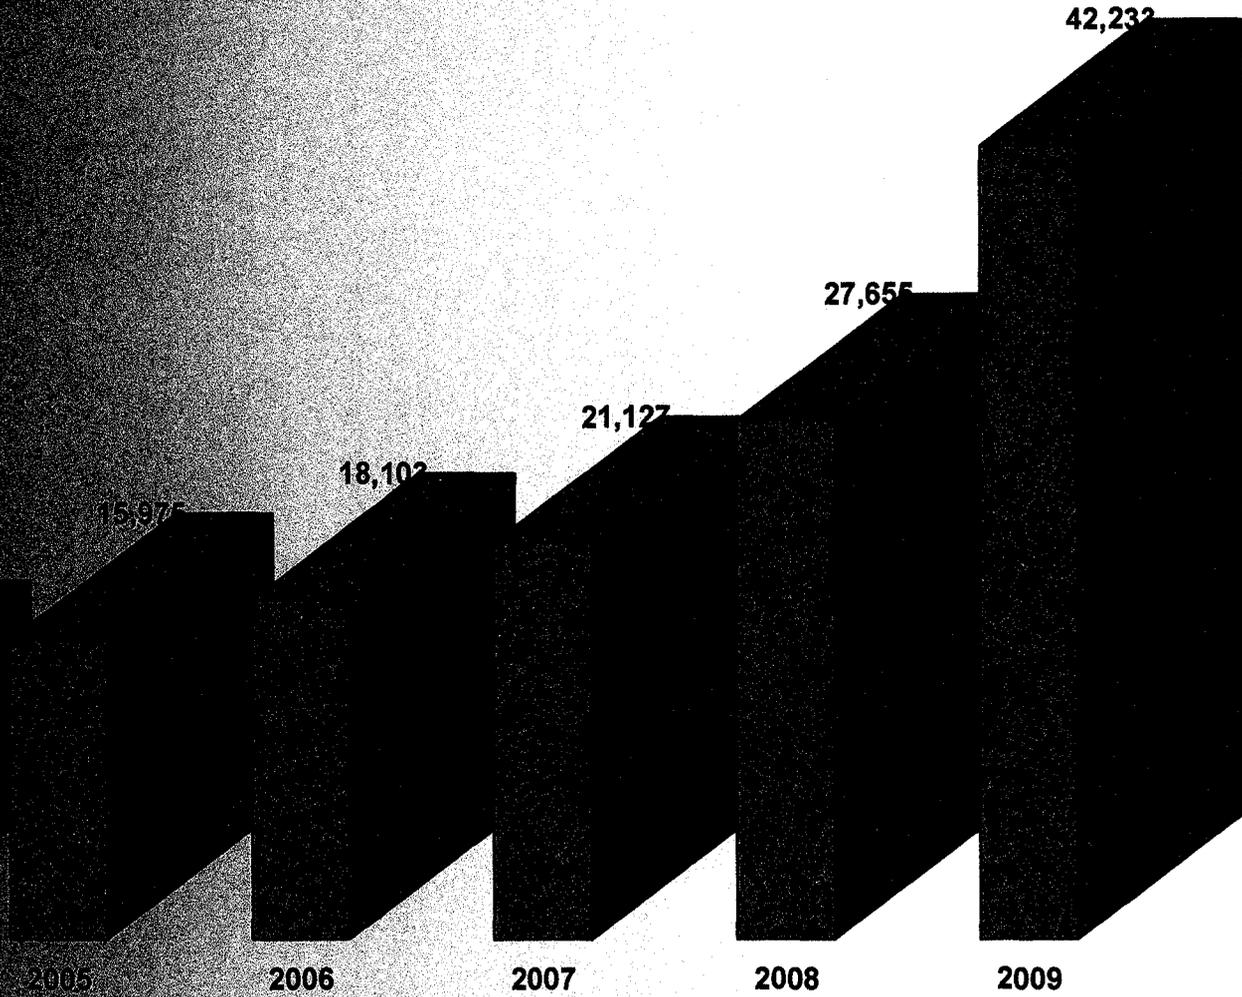

ATTACHMENT E
PROGRESS REPORT
PLEVNA

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	2/1/2008
Preliminary Engineering	4/2008
Preliminary Environmental Review	5/2008
Preliminary Cultural Impact Review	5/2008
Preliminary Historical Impact Review	5/2008
Preliminary Geophysical Review	5/2008
Real Property - Site Procurement	
Ownership Report from Title Company	7/2008
Discussions with Landowner	7/2008
Documentation of site use arrangements	7/2008
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	7/2008
Federal Communications Commission (FCC)	
Antenna Structure Registration	N/A
Attorney to file cellular Phase II Application w/FCC	8/2008
FCC Public Notice -- cellular	8/2008
FCC approval notice -- cellular	10/2008
Cellular license issued by FCC	10/2008
Site interconnection arrangements	N/A
If microwave coordination:	N/A
Attorney to file microwave application w/FCC	N/A
FCC Public Notice -- microwave	N/A
FCC approval notice -- microwave	N/A
Microwave license issued by FCC	N/A
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	N/A
Submit cellular radio installation specifications & contract to contractors for quotes	N/A
Finalize cellular contract	N/A
Contractor to install cellular radio	10/2008
Prepare microwave radio installation specifications & contract	N/A
Submit microwave radio installation specifications & contract to contractors for quotes	N/A
Finalize microwave contract	N/A
Contractor to install microwave radio	N/A
Prepare misc. equipment, hardware and power plant specifications	N/A
Purchase misc. equipment, hardware and power plant	N/A
Delivery of misc. equipment, hardware and power plant	N/A
MRC personnel to install misc. equipment, hardware and power plant	N/A

ATTACHMENT E
PROGRESS REPORT

PLEVNA

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	N/A
Foundation & gen. slab installation by MRC personnel	N/A
Prepare building specifications & contract	N/A
Submit building specifications & contract to contractors for quotes	N/A
Finalize contract to purchase building	N/A
Building delivery to MRC Supply	N/A
Quotes for Offloading Building	N/A
Offload Building	N/A
Rekey Building	N/A
Quotes for MRTC Sign	N/A
MRTC Sign Installation	N/A
Site development & landscaping by MRC personnel	10/2008
Provide building information to COE/Network Engineer for inclusion in company database	N/A
Tower	
Obtain structural analysis of existing tower, if any	N/A
Prepare tower and antenna specifications & contract	4/2008
Submit tower and antenna specifications & contract to contractors w/request for quotes	4/2008
Finalize contract	7/2008
Contractor to complete contract & install tower and antenna(s)	9/2008
Contractor to post antenna structure registration number on tower	9/2008
Generator	
Purchase Generator, ATS	N/A
Delivery of Generator, ATS	N/A
Test & Turn-up Generator	N/A
Provide generator information to COE/Network Engineer for inclusion in company database	N/A
Power	
Provide local power utility company information on electrical line required	N/A
Power utility company Install electrical lines	N/A
Provide local power utility company information on gas line requirements	N/A
Power utility company install gas lines	N/A
Misc. Electrical Contract	
Quotes for Misc. Electrical	N/A
Award Contract	N/A
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	10/2008
Contractor to Provide Warranty Info on Installed Equipment	10/2008
Estimated Completion Date	10/15/2008

ATTACHMENT F
PROGRESS REPORT
LAMBERT 2-WAY

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	7/2008
Preliminary Engineering	7/2008
Preliminary Environmental Review	
Preliminary Cultural Impact Review	
Preliminary Historical Impact Review	
Preliminary Geophysical Review	
Real Property - Site Procurement	
Ownership Report from Title Company	In Place
Discussions with Landowner	In Place
Documentation of site use arrangements	In Place
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	9/2008
Federal Communications Commission (FCC)	
Antenna Structure Registration	N/A
Attorney to file cellular Phase II Application w/FCC	11/2008
FCC Public Notice -- cellular	11/2008
FCC approval notice -- cellular	12/2008
Cellular license issued by FCC	12/2008
Site interconnection arrangements	N/A
If microwave coordination:	N/A
Attorney to file microwave application w/FCC	N/A
FCC Public Notice -- microwave	N/A
FCC approval notice -- microwave	N/A
Microwave license issued by FCC	N/A
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	11/2008
Submit cellular radio installation specifications & contract to contractors for quotes	11/2008
Finalize cellular contract	12/2008
Contractor to install cellular radio	1/2009
Prepare microwave radio installation specifications & contract	8/2008
Submit microwave radio installation specifications & contract to contractors for quotes	8/2008
Finalize microwave contract	9/2008
Contractor to install microwave radio	1/2009
Prepare misc. equipment, hardware and power plant specifications	8/2008
Purchase misc. equipment, hardware and power plant	9/2008
Delivery of misc. equipment, hardware and power plant	11/2008
MRC personnel to install misc. equipment, hardware and power plant	12/2008

ATTACHMENT F
PROGRESS REPORT
LAMBERT 2-WAY

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	N/A
Foundation & gen. slab installation by MRC personnel	N/A
Prepare building specifications & contract	N/A
Submit building specifications & contract to contractors for quotes	N/A
Finalize contract to purchase building	N/A
Building delivery to MRC Supply	N/A
Quotes for Offloading Building	N/A
Offload Building	N/A
Rekey Building	N/A
Quotes for MRTC Sign	N/A
MRTC Sign Installation	N/A
Site development & landscaping by MRC personnel	N/A
Provide building information to COE/Network Engineer for inclusion in company database	N/A
Tower	
Obtain structural analysis of existing tower, if any	9/2008
Prepare tower and antenna specifications & contract	9/2008
Submit tower and antenna specifications & contract to contractors w/request for quotes	9/2008
Finalize contract	10/2008
Contractor to complete contract & install tower and antenna(s)	11/2008
Contractor to post antenna structure registration number on tower	N/A
Generator	
Purchase Generator, ATS	N/A
Delivery of Generator, ATS	N/A
Test & Turn-up Generator	N/A
Provide generator information to COE/Network Engineer for inclusion in company database	N/A
Power	
Provide local power utility company information on electrical line required	N/A
Power utility company Install electrical lines	N/A
Provide local power utility company information on gas line requirements	N/A
Power utility company install gas lines	N/A
Misc. Electrical Contract	
Quotes for Misc. Electrical	N/A
Award Contract	N/A
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	10/2008
Contractor to Provide Warranty Info on Installed Equipment	10/2008
Estimated Completion Date	12/2008

ATTACHMENT G
PROGRESS REPORT
MCGUIRE CREEK

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	1/2008
Preliminary Engineering	5/2008
Preliminary Environmental Review	5/2008
Preliminary Cultural Impact Review	5/2008
Preliminary Historical Impact Review	5/2008
Preliminary Geophysical Review	5/2008
Real Property - Site Procurement	
Ownership Report from Title Company	N/A
Discussions with Landowner	5/2008
Documentation of site use arrangements	6/3/2008
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	5/3/2008
Federal Communications Commission (FCC)	
Antenna Structure Registration	N/A
Attorney to file cellular Phase II Application w/FCC	6/23/2008
FCC Public Notice -- cellular	7/2008
FCC approval notice -- cellular	9/2008
Cellular license issued by FCC	9/2008
Site interconnection arrangements	6/3/2008
If microwave coordination:	N/A
Attorney to file microwave application w/FCC	N/A
FCC Public Notice -- microwave	N/A
FCC approval notice -- microwave	N/A
Microwave license issued by FCC	N/A
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	8/2008
Submit cellular radio installation specifications & contract to contractors for quotes	8/2008
Finalize cellular contract	8/2008
Contractor to install cellular radio	9/2008
Prepare microwave radio installation specifications & contract	N/A
Submit microwave radio installation specifications & contract to contractors for quotes	N/A
Finalize microwave contract	N/A
Contractor to install microwave radio	N/A
Prepare misc. equipment, hardware and power plant specifications	5/2008
Purchase misc. equipment, hardware and power plant	5/28/2008
Delivery of misc. equipment, hardware and power plant	7/2008
MRC personnel to install misc. equipment, hardware and power plant	8/2008

ATTACHMENT G
PROGRESS REPORT
MCGUIRE CREEK

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	6/4/2008
Foundation & gen. slab installation by MRC personnel	7/2008
Prepare building specifications & contract	in stock
Submit building specifications & contract to contractors for quotes	in stock
Finalize contract to purchase building	in stock
Building delivery to MRC Supply	in stock
Quotes for Offloading Building	in stock
Offload Building	in stock
Rekey Building	7/2008
Quotes for MRTC Sign	5/28/08
MRTC Sign Installation	8/2008
Site development & landscaping by MRC personnel	9/2008
Provide building information to COE/Network Engineer for inclusion in company database	7/2008
Tower	
Obtain structural analysis of existing tower, if any	N/A
Prepare tower and antenna specifications & contract	5/2008
Submit tower and antenna specifications & contract to contractors w/request for quotes	5/2008
Finalize contract	7/2008
Contractor to complete contract & install tower and antenna(s)	7/2008
Contractor to post antenna structure registration number on tower	7/2008
Generator	
Purchase Generator, ATS	5/28/2008
Delivery of Generator, ATS	7/2008
Test & Turn-up Generator	8/2008
Provide generator information to COE/Network Engineer for inclusion in company database	7/2008
Power	
Provide local power utility company information on electrical line required	4/2008
Power utility company Install electrical lines	6/2008
Provide local power utility company information on gas line requirements	N/A
Power utility company install gas lines	N/A
Misc. Electrical Contract	
Quotes for Misc. Electrical	5/2008
Award Contract	6/2008
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	7/2008
Contractor to Provide Warranty Info on Installed Equipment	8/2008
Estimated Completion Date	9/31/2008

ATTACHMENT H
PROGRESS REPORT
OTTER CREEK

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	2006
Preliminary Engineering	9/2008
Preliminary Environmental Review	9/2008
Preliminary Cultural Impact Review	9/2008
Preliminary Historical Impact Review	9/2008
Preliminary Geophysical Review	9/2008
Real Property - Site Procurement	
Ownership Report from Title Company	10/2008
Discussions with Landowner	10/2008
Documentation of site use arrangements	10/2008
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	9/2008
Federal Communications Commission (FCC)	
Antenna Structure Registration	
Attorney to file cellular Phase II Application w/FCC	11/2008
FCC Public Notice -- cellular	11/2008
FCC approval notice -- cellular	12/2008
Cellular license issued by FCC	12/2008
Site interconnection arrangements	
If microwave coordination:	9/2008
Attorney to file microwave application w/FCC	11/2008
FCC Public Notice -- microwave	11/2008
FCC approval notice -- microwave	12/2008
Microwave license issued by FCC	12/2008
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	11/2008
Submit cellular radio installation specifications & contract to contractors for quotes	11/2008
Finalize cellular contract	12/2008
Contractor to install cellular radio	12/2008
Prepare microwave radio installation specifications & contract	8/2008
Submit microwave radio installation specifications & contract to contractors for quotes	8/2008
Finalize microwave contract	9/2008
Contractor to install microwave radio	12/2008
Prepare misc. equipment, hardware and power plant specifications	8/2008
Purchase misc. equipment, hardware and power plant	9/2008
Delivery of misc. equipment, hardware and power plant	11/2008
MRC personnel to install misc. equipment, hardware and power plant	12/2008

ATTACHMENT H
PROGRESS REPORT
OTTER CREEK

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	9/2008
Foundation & gen. slab installation by MRC personnel	10/2008
Prepare building specifications & contract	In Stock
Submit building specifications & contract to contractors for quotes	In Stock
Finalize contract to purchase building	In Stock
Building delivery to MRC Supply	In Stock
Quotes for Offloading Building	9/2008
Offload Building	11/2008
Rekey Building	11/2008
Quotes for MRTC Sign	9/2008
MRTC Sign Installation	11/2008
Site development & landscaping by MRC personnel	12/2008
Provide building information to COE/Network Engineer for inclusion in company database	11/2008
Tower	
Obtain structural analysis of existing tower, if any	9/2008
Prepare tower and antenna specifications & contract	9/2008
Submit tower and antenna specifications & contract to contractors w/request for quotes	9/2008
Finalize contract	10/2008
Contractor to complete contract & install tower and antenna(s)	12/2008
Contractor to post antenna structure registration number on tower	12/2008
Generator	
Purchase Generator, ATS	9/2008
Delivery of Generator, ATS	11/2008
Test & Turn-up Generator	12/2008
Provide generator information to COE/Network Engineer for inclusion in company database	11/2008
Power	
Provide local power utility company information on electrical line required	9/2008
Power utility company Install electrical lines	10/2008
Provide local power utility company information on gas line requirements	N/A
Power utility company install gas lines	N/A
Misc. Electrical Contract	
Quotes for Misc. Electrical	8/2008
Award Contract	9/2008
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	11/2008
Contractor to Provide Warranty Info on Installed Equipment	11/2008
Estimated Completion Date	
	12/2008

ATTACHMENT I
PROGRESS REPORT
NORTH COHAGEN

ACTION ITEM	COMPLETE DATE
Preliminary Analysis	
Initial Site Analysis	1/3/2008
Preliminary Engineering	5/2008
Preliminary Environmental Review	5/2008
Preliminary Cultural Impact Review	5/2008
Preliminary Historical Impact Review	5/2008
Preliminary Geophysical Review	5/2008
Real Property - Site Procurement	
Ownership Report from Title Company	4/22/2008
Discussions with Landowner	4/15/2008
Documentation of site use arrangements	6/13/2008
Federal Aviation Administration (FAA)	
MRC gather information and prepare Notice of Proposed Construction or Alteration (FAA Form 7460-1)	5/3/2008
Federal Communications Commission (FCC)	
Antenna Structure Registration	N/A
Attorney to file cellular Phase II Application w/FCC	7/2008
FCC Public Notice -- cellular	7/2008
FCC approval notice -- cellular	9/2008
Cellular license issued by FCC	9/2008
Site interconnection arrangements	N/A
If microwave coordination:	N/A
Attorney to file microwave application w/FCC	N/A
FCC Public Notice -- microwave	N/A
FCC approval notice -- microwave	N/A
Microwave license issued by FCC	N/A
Engineering - MRC (in house)	
Prepare cellular radio installation specifications & contract	8/2008
Submit cellular radio installation specifications & contract to contractors for quotes	8/2008
Finalize cellular contract	8/2008
Contractor to install cellular radio	9/2008
Prepare microwave radio installation specifications & contract	5/16/2008
Submit microwave radio installation specifications & contract to contractors for quotes	5/16/2008
Finalize microwave contract	6/9/2008
Contractor to install microwave radio	8/2008
Prepare misc. equipment, hardware and power plant specifications	5/2008
Purchase misc. equipment, hardware and power plant	5/28/2008
Delivery of misc. equipment, hardware and power plant	7/2008
MRC personnel to install misc. equipment, hardware and power plant	8/2008

ATTACHMENT I
PROGRESS REPORT
NORTH COHAGEN

ACTION ITEM	COMPLETE DATE
Building	
Building permit (local and/or state)	6/4/2008
Foundation & gen. slab installation by MRC personnel	7/2008
Prepare building specifications & contract	in stock
Submit building specifications & contract to contractors for quotes	in stock
Finalize contract to purchase building	in stock
Building delivery to MRC Supply	in stock
Quotes for Offloading Building	in stock
Offload Building	in stock
Rekey Building	7/2008
Quotes for MRTC Sign	5/28/08
MRTC Sign Installation	8/2008
Site development & landscaping by MRC personnel	9/2008
Provide building information to COE/Network Engineer for inclusion in company database	7/2008
Tower	
Obtain structural analysis of existing tower, if any	5/5/2008
Prepare tower and antenna specifications & contract	5/2008
Submit tower and antenna specifications & contract to contractors w/request for quotes	5/2008
Finalize contract	7/2008
Contractor to complete contract & install tower and antenna(s)	7/2008
Contractor to post antenna structure registration number on tower	7/2008
Generator	
Purchase Generator, ATS	5/28/2008
Delivery of Generator, ATS	7/2008
Test & Turn-up Generator	8/2008
Provide generator information to COE/Network Engineer for inclusion in company database	7/2008
Power	
Provide local power utility company information on electrical line required	4/2008
Power utility company Install electrical lines	7/2008
Provide local power utility company information on gas line requirements	N/A
Power utility company install gas lines	N/A
Misc. Electrical Contract	
Quotes for Misc. Electrical	5/2008
Award Contract	6/2008
Notify Contractor of Bldg, Gen., Power & Gas Placement & to Begin Work	7/2008
Contractor to Provide Warranty Info on Installed Equipment	8/2008
Estimated Completion Date	
	9/31/2008
